LCS Number	Date Reading Collected	Measured Liquid Level Above Transducer (Ft.)	Transducer Height above Floor of Quarry (Ft.)	Base of Sump Elevation (Ft. MSL)	Height of Liquid (Ft.)	Elevation of Leachate (Ft. MSL)	Compliance Level (Ft. Above Quarry Floor)	Pump on during measurement? (Y/N)	Technician initials	Liquid level meter used	Comments
LCS- 1D	3/27/13	25.9	12.0	252.22	37.9	290.12	30.00	Y	Herst - J. Wilkinson	Dedicated Transducer	
LCS- 1D	4/8/13	86.1	12.0	252.22	98.1	350.32	30.00	N	B. Sehie	Dedicated Transducer	Storage Restriction - Pump Off
LCS- 1D	4/15/13	NA	12.0	252.22			30.00	N	Herst - M. Stewart	Dedicated Transducer	LCS Offline for Electrical Service
LCS- 1D	4/22/13	NA	12.0	252.22			30.00	N	B. Sehie	Dedicated Transducer	LCS Offline for Electrical Service
LCS- 1D	4/29/13	15.6	12.0	252.22	27.6	279.82	30.00	Y	B. Sehie	Dedicated Transducer	
LCS- 1D	5/6/13	15.2	12.0	252.22	27.2	279.42	30.00	Y	Herst - M. Stewart	Dedicated Transducer	
LCS- 1D	5/13/13	15.0	12.0	252.22	27.0	279.22	30.00	Y	B. Sehie	Dedicated Transducer	
LCS- 1D	5/20/13	14.9	12.0	252.22	26.9	279.12	30.00	Y	B. Sehie	Dedicated Transducer	
LCS- 1D	5/27/13	15.4	12.0	252.22	27.4	279.62	30.00	Y	B. Sehie	Dedicated Transducer	
LCS- 1D	6/3/13	14.8	12.0	252.22	26.8	279.02	30.00	Y	B. Sehie	Dedicated Transducer	
LCS- 1D	6/10/13	14.9	12.0	252.22	26.9	279.12	30.00	Y	B. Sehie	Dedicated Transducer	
LCS- 1D	6/17/13	14.9	12.0	252.22	26.9	279.12	30.00	Y	Herst - M. Stewart	Dedicated Transducer	
LCS- 1D	6/24/13	74.8	12.0	252.22	86.8	339.02	30.00	N	B. Sehie	Dedicated Transducer	Motor Failure - replacement schd. 7/1/13

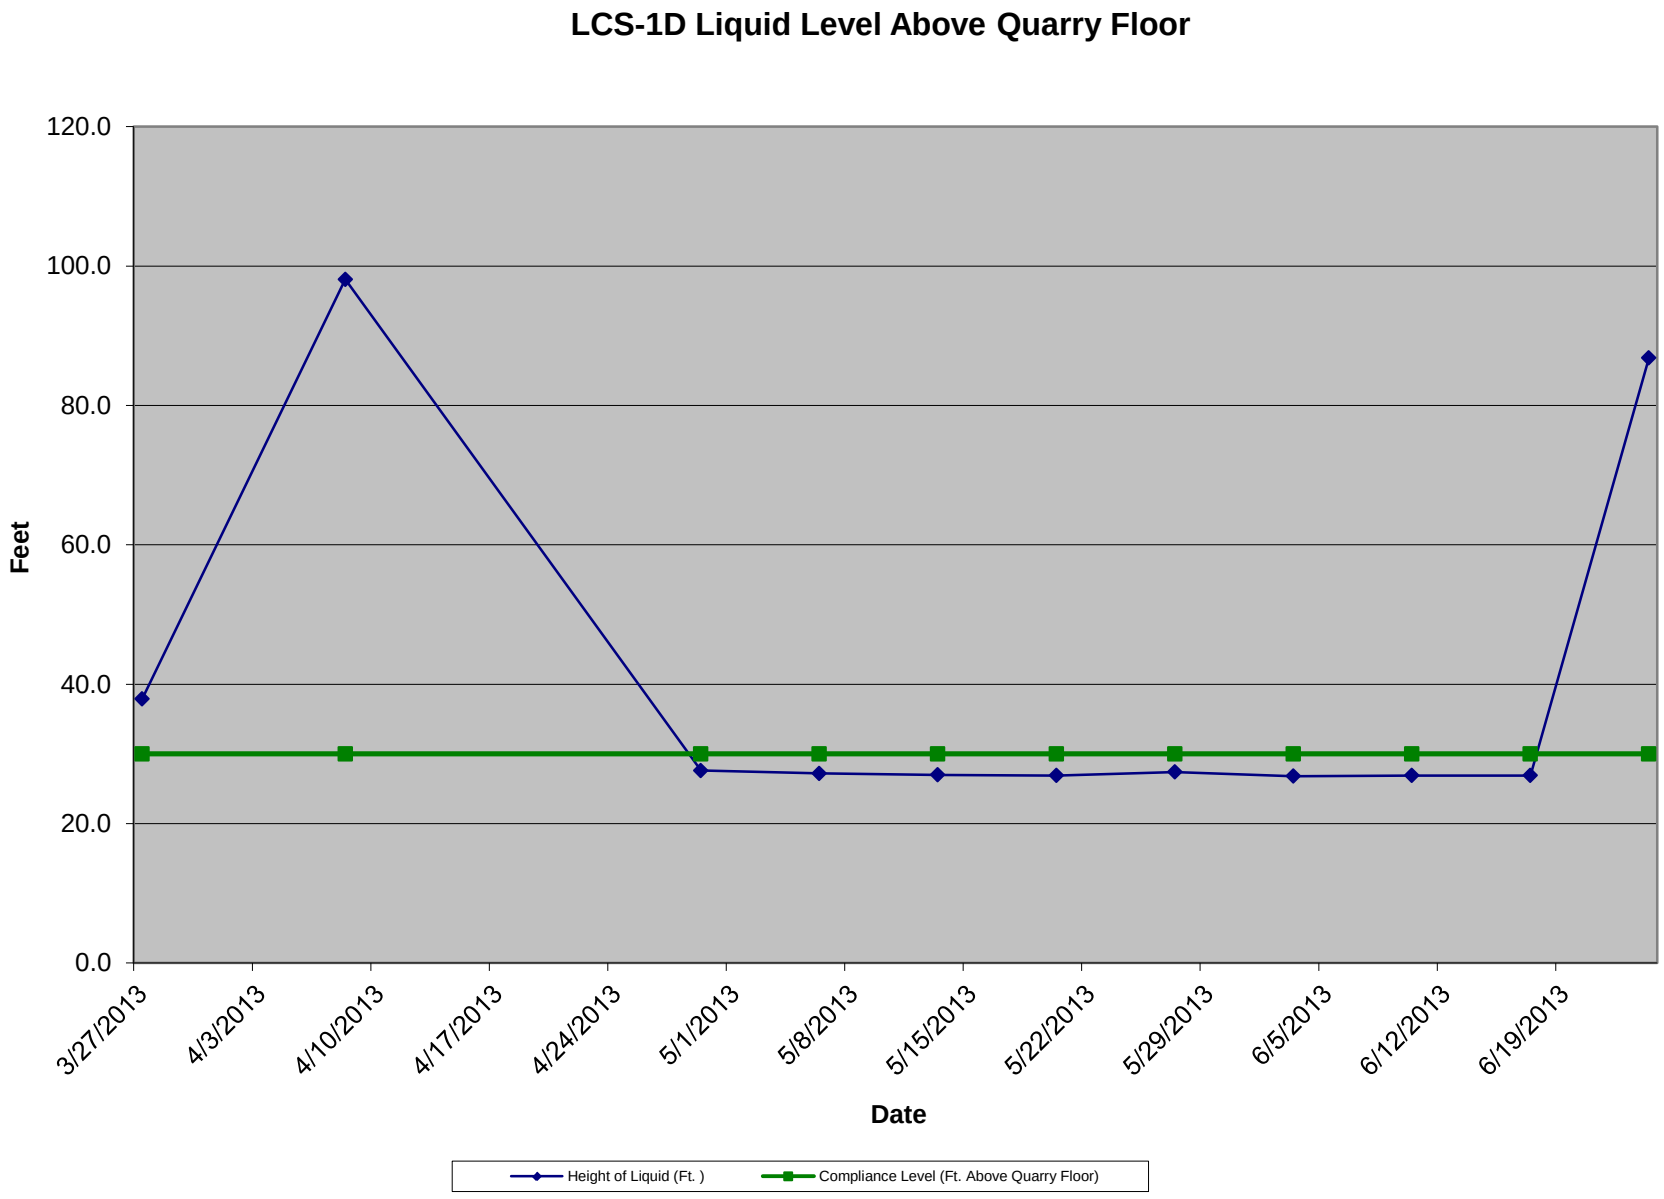
LCS-1D Liquid Level Above Quarry Floor
120.0
100.0
80.0
60.0
40.0
20.0
0.0
Feet
3/27/2013
4/3/2013
4/10/2013
4/17/2013
4/24/2013
5/1/2013
5/8/2013
5/15/2013
5/22/2013
5/29/2013
6/5/2013
6/12/2013
6/19/2013
Date
Height of Liquid (Ft.)
Compliance Level (Ft. Above Quarry Floor)

LCS Number	Date Reading Collected	Measured Liquid Level Above Transducer (Ft.)	Transducer Height above Floor of Quarry (Ft.)	Base of Sump Elevation (Ft. MSL)	Height of Liquid (Ft.)	Elevation of Leachate (Ft. MSL)	Compliance Level (Ft. Above Quarry Floor)	Pump on during measurement? (Y/N)	Technician initials	Liquid level meter used	Comments
LCS- 2D	3/27/13	13.4	14.4	235.92	27.8	263.72	30.00	Y	Herst - J. Wilkinson	Dedicated Transducer	
LCS- 2D	4/8/13	144.5	14.4	235.92	158.9	394.82	30.00	N	B. Sehie	Dedicated Transducer	Storage Restriction - Pump Off
LCS- 2D	4/15/13	13.6	14.4	235.92	28.0	263.92	30.00	Y	Herst - M. Stewart	Dedicated Transducer	
LCS- 2D	4/22/13	13.5	14.4	235.92	27.9	263.82	30.00	Y	B. Sehie	Dedicated Transducer	
LCS- 2D	4/29/13	13.6	14.4	235.92	28.0	263.92	30.00	Y	B. Sehie	Dedicated Transducer	
LCS- 2D	5/6/13	13.5	14.4	235.92	27.9	263.82	30.00	Y	Herst - M. Stewart	Dedicated Transducer	
LCS- 2D	5/13/13	13.3	14.4	235.92	27.7	263.62	30.00	Y	B. Sehie	Dedicated Transducer	
LCS- 2D	5/20/13	13.7	14.4	235.92	28.1	264.02	30.00	Y	B. Sehie	Dedicated Transducer	
LCS- 2D	5/27/13	13.9	14.4	235.92	28.3	264.22	30.00	Y	B. Sehie	Dedicated Transducer	
LCS- 2D	6/3/13	13.8	14.4	235.92	28.2	264.12	30.00	Y	B. Sehie	Dedicated Transducer	
LCS- 2D	6/10/13	13.6	14.4	235.92	28.0	263.92	30.00	Y	B. Sehie	Dedicated Transducer	
LCS- 2D	6/17/13	13.4	14.4	235.92	27.8	263.72	30.00	Y	Herst - M. Stewart	Dedicated Transducer	
LCS- 2D	6/24/13	13.8	14.4	235.92	28.2	264.12	30.00	Y	B. Sehie	Dedicated Transducer	

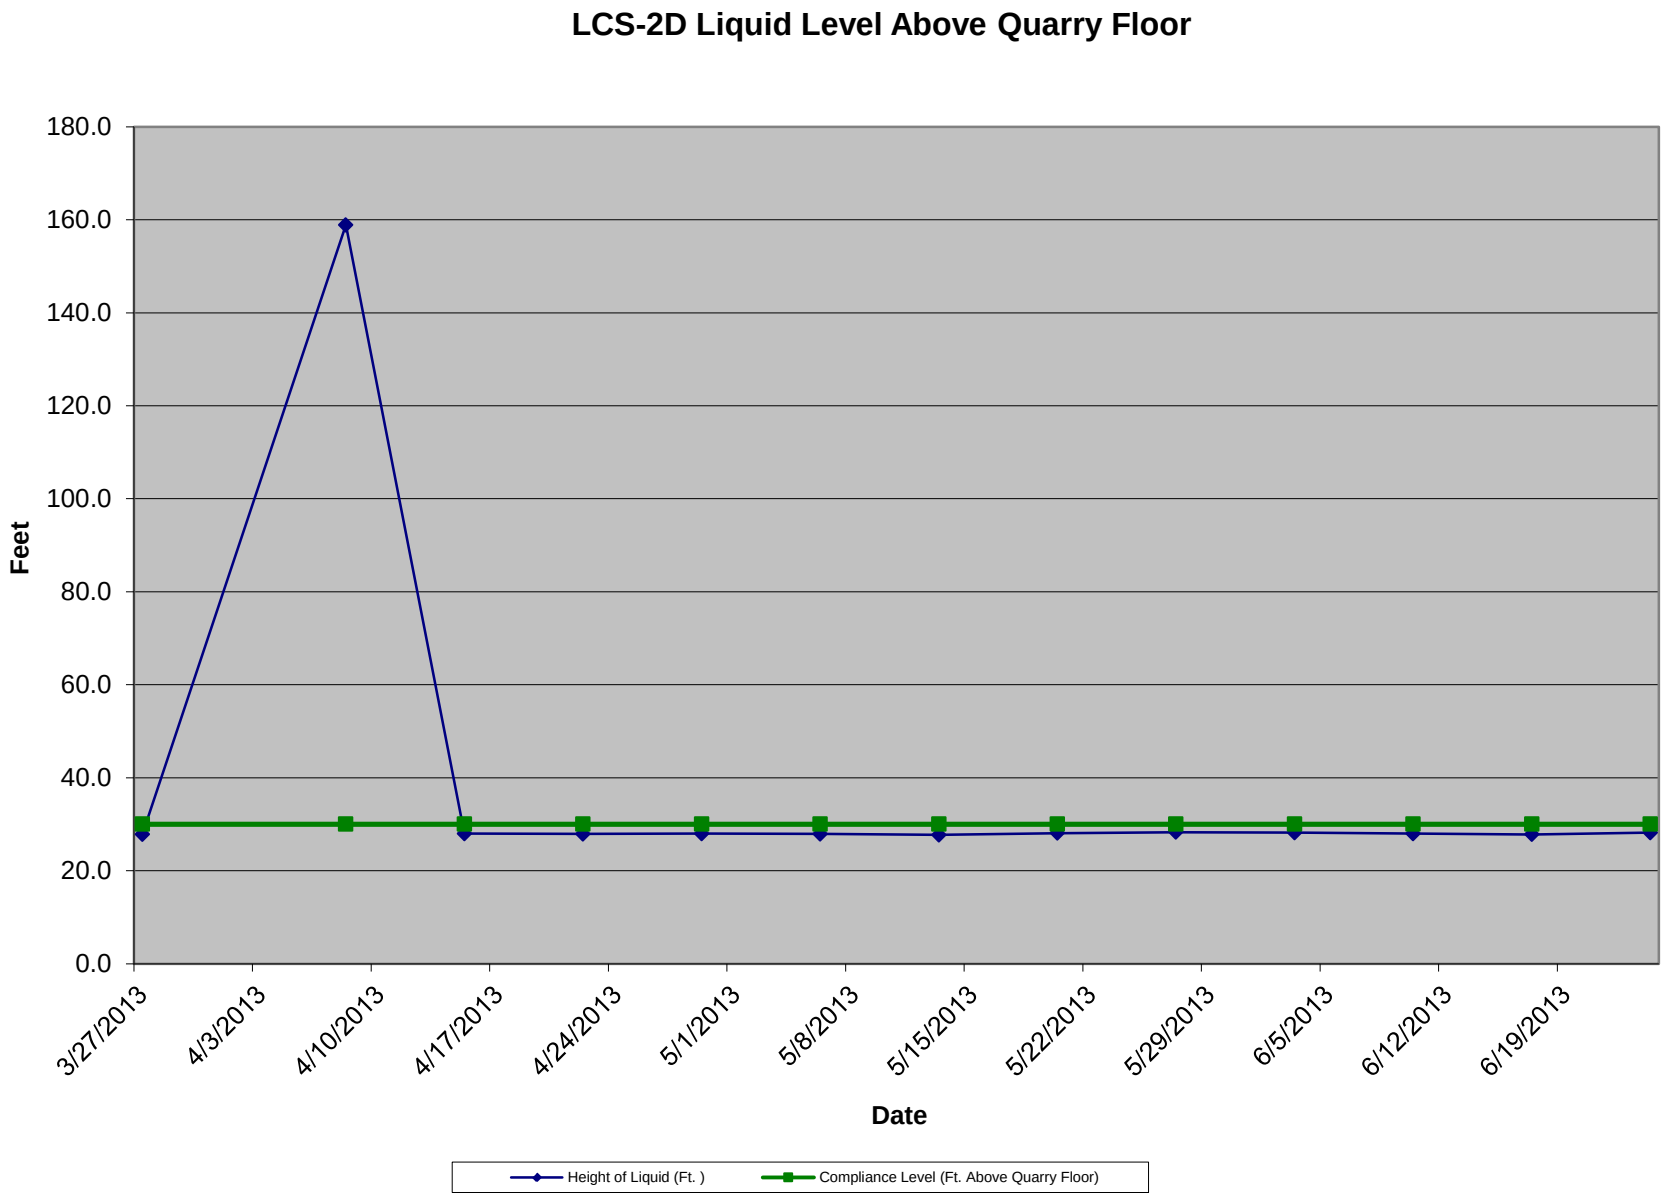
LCS-2D Liquid Level Above Quarry Floor
180.0
160.0
140.0
120.0
100.0
80.0
60.0
40.0
20.0
0.0
Feet
3/27/2013
4/3/2013
4/10/2013
4/17/2013
4/24/2013
5/1/2013
5/8/2013
5/15/2013
5/22/2013
5/29/2013
6/5/2013
6/12/2013
6/19/2013
Date
Height of Liquid (Ft.)
Compliance Level (Ft. Above Quarry Floor)

LCS Number	Date Reading Collected	Measured Liquid Level Above Transducer (Ft.)	Transducer Height above Floor of Quarry (Ft.)	Base of Sump Elevation (Ft. MSL)	Height of Liquid (Ft.)	Elevation of Leachate (Ft. MSL)	Compliance Level (Ft. Above Quarry Floor)	Pump on during measurement? (Y/N)	Technician initials	Liquid level meter used	Comments
LCS- 3C	3/27/13					N/A	30.00	N/A	Herst - J. Wilkinson	N/A	Non-Operational
LCS- 3C	4/8/13					N/A	30.00	N/A	B. Sehie	N/A	Non-Operational
LCS- 3C	4/15/13					N/A	30.00	N/A	Herst - M. Stewart	N/A	Non-Operational
LCS- 3C	4/22/13					N/A	30.00	N/A	B. Sehie	N/A	Non-Operational
LCS- 3C	4/29/13					0.00	30.00	N/A	B. Sehie	N/A	Non-Operational
LCS- 3C	5/6/13					0.00	30.00	N/A	Herst - M. Stewart	N/A	Non-Operational
LCS- 3C	5/13/13					0.00	30.00	N/A	B. Sehie	N/A	Non-Operational
LCS- 3C	5/20/13					0.00	30.00	N/A	B. Sehie	N/A	Non-Operational
LCS- 3C	5/27/13					0.00	30.00	N/A	B. Sehie	N/A	Non-Operational
LCS- 3C	6/3/13					0.00	30.00	N/A	B. Sehie	N/A	Non-Operational
LCS- 3C	6/10/13					0.00	30.00	N/A	B. Sehie	N/A	Non-Operational
LCS- 3C	6/17/13					0.00	30.00	N/A	Herst - M. Stewart	N/A	Non-Operational
LCS- 3C	6/24/13					0.00	30.00	N/A	B. Sehie	N/A	Non-Operational

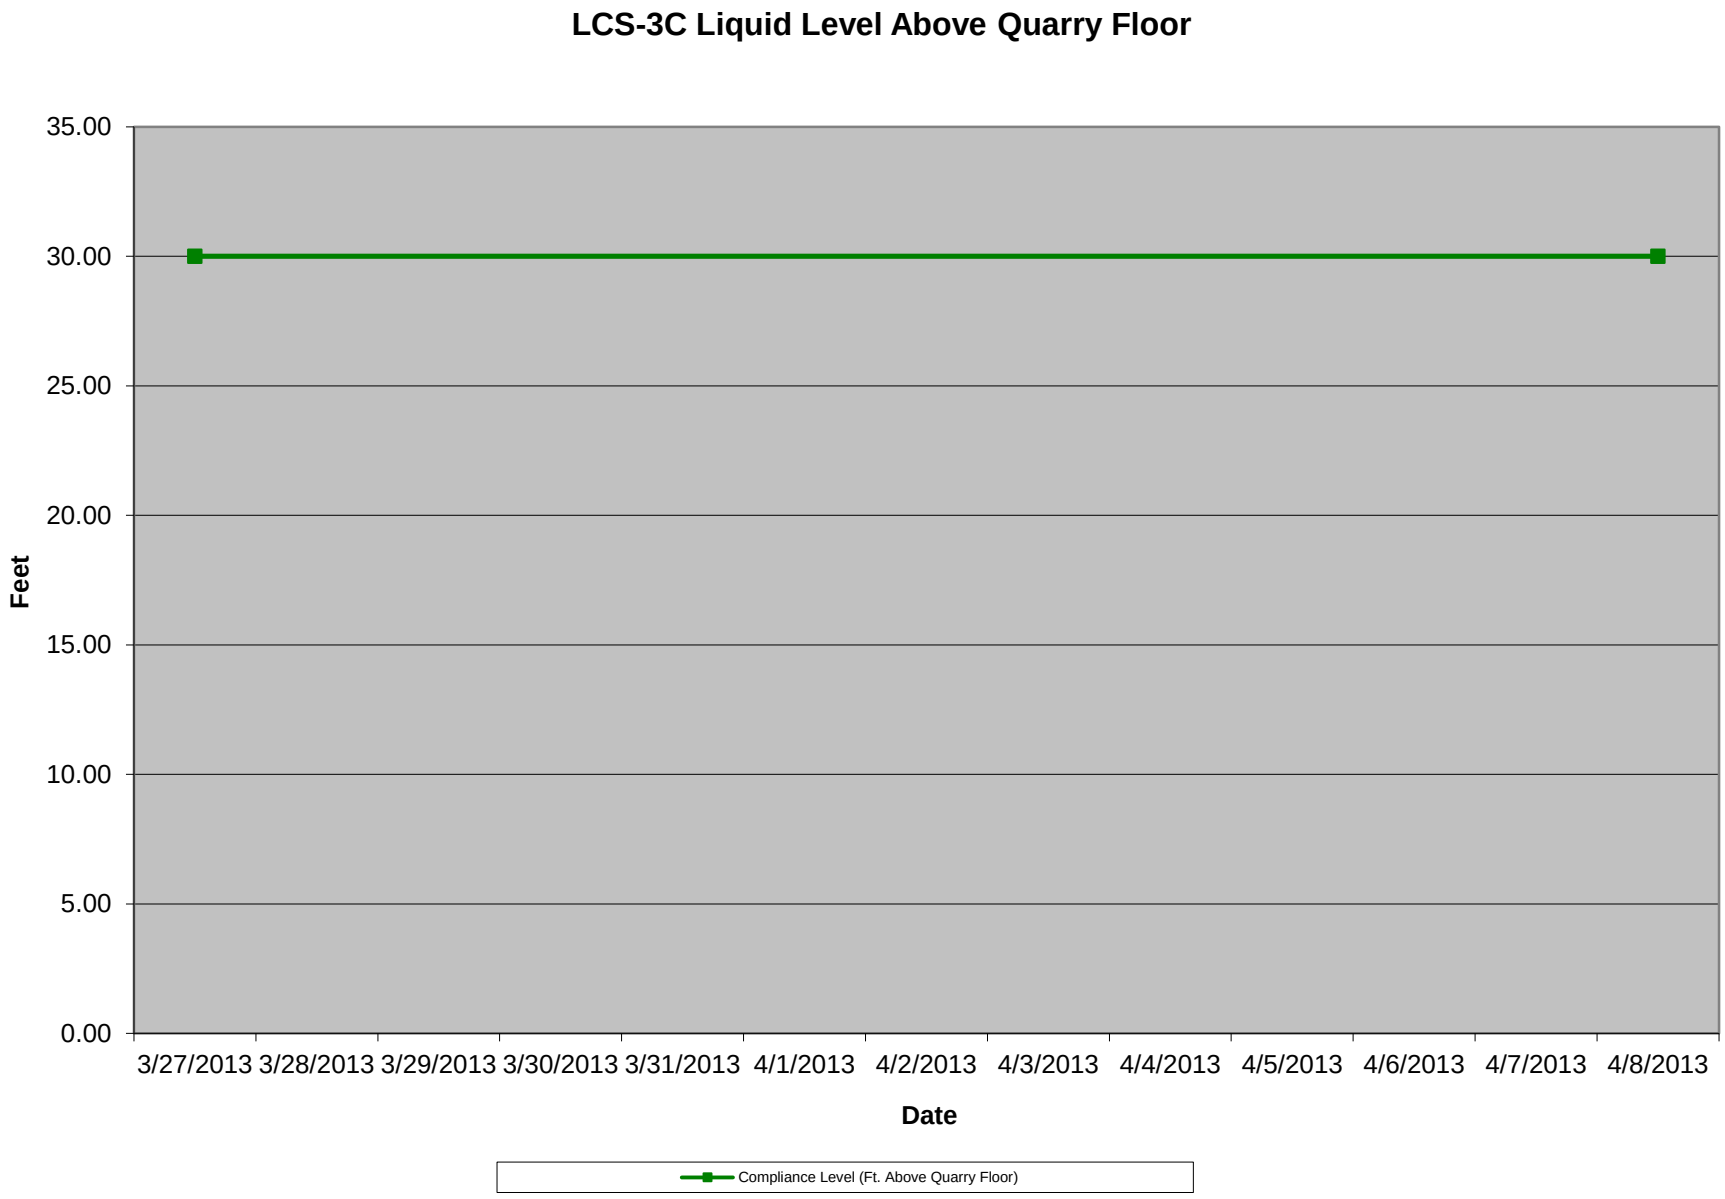
LCS-3C Liquid Level Above Quarry Floor
35.00
30.00
25.00
20.00
15.00
10.00
5.00
0.00
Feet
3/27/2013
3/28/2013
3/29/2013
3/30/2013
3/31/2013
4/1/2013
4/2/2013
4/3/2013
4/4/2013
4/5/2013
4/6/2013
4/7/2013
4/8/2013
Date
Compliance Level (Ft. Above Quarry Floor)

LCS Number	Date Reading Collected	Measured Liquid Level Above Transducer (Ft.)	Transducer Height above Floor of Quarry (Ft.)	Base of Sump Elevation (Ft. MSL)	Height of Liquid (Ft.)	Elevation of Leachate (Ft. MSL)	Compliance Level (Ft. Above Quarry Floor)	Pump on during measurement? (Y/N)	Technician initials	Liquid level meter used	Comments
LCS- 4B	3/27/13					N/A	30.00	N/A	Herst - J. Wilkinson	N/A	Non-Operational
LCS- 4B	4/8/13					N/A	30.00	N/A	B. Sehie	N/A	Non-Operational
LCS- 4B	4/15/13					N/A	30.00	N/A	Herst - M. Stewart	N/A	Non-Operational
LCS- 4B	4/22/13					N/A	30.00	N/A	B. Sehie	N/A	Non-Operational
LCS- 4B	4/29/13					0.00	30.00	N/A	B. Sehie	N/A	Non-Operational
LCS- 4B	5/6/13					0.00	30.00	N/A	Herst - M. Stewart	N/A	Non-Operational
LCS- 4B	5/13/13					0.00	30.00	N/A	B. Sehie	N/A	Non-Operational
LCS- 4B	5/20/13					0.00	30.00	N/A	B. Sehie	N/A	Non-Operational
LCS- 4B	5/27/13					0.00	30.00	N/A	B. Sehie	N/A	Non-Operational
LCS- 4B	6/3/13					0.00	30.00	N/A	B. Sehie	N/A	Non-Operational
LCS- 4B	6/10/13					0.00	30.00	N/A	B. Sehie	N/A	Non-Operational
LCS- 4B	6/17/13					0.00	30.00	N/A	Herst - M. Stewart	N/A	Non-Operational
LCS- 4B	6/24/13					0.00	30.00	N/A	B. Sehie	N/A	Non-Operational

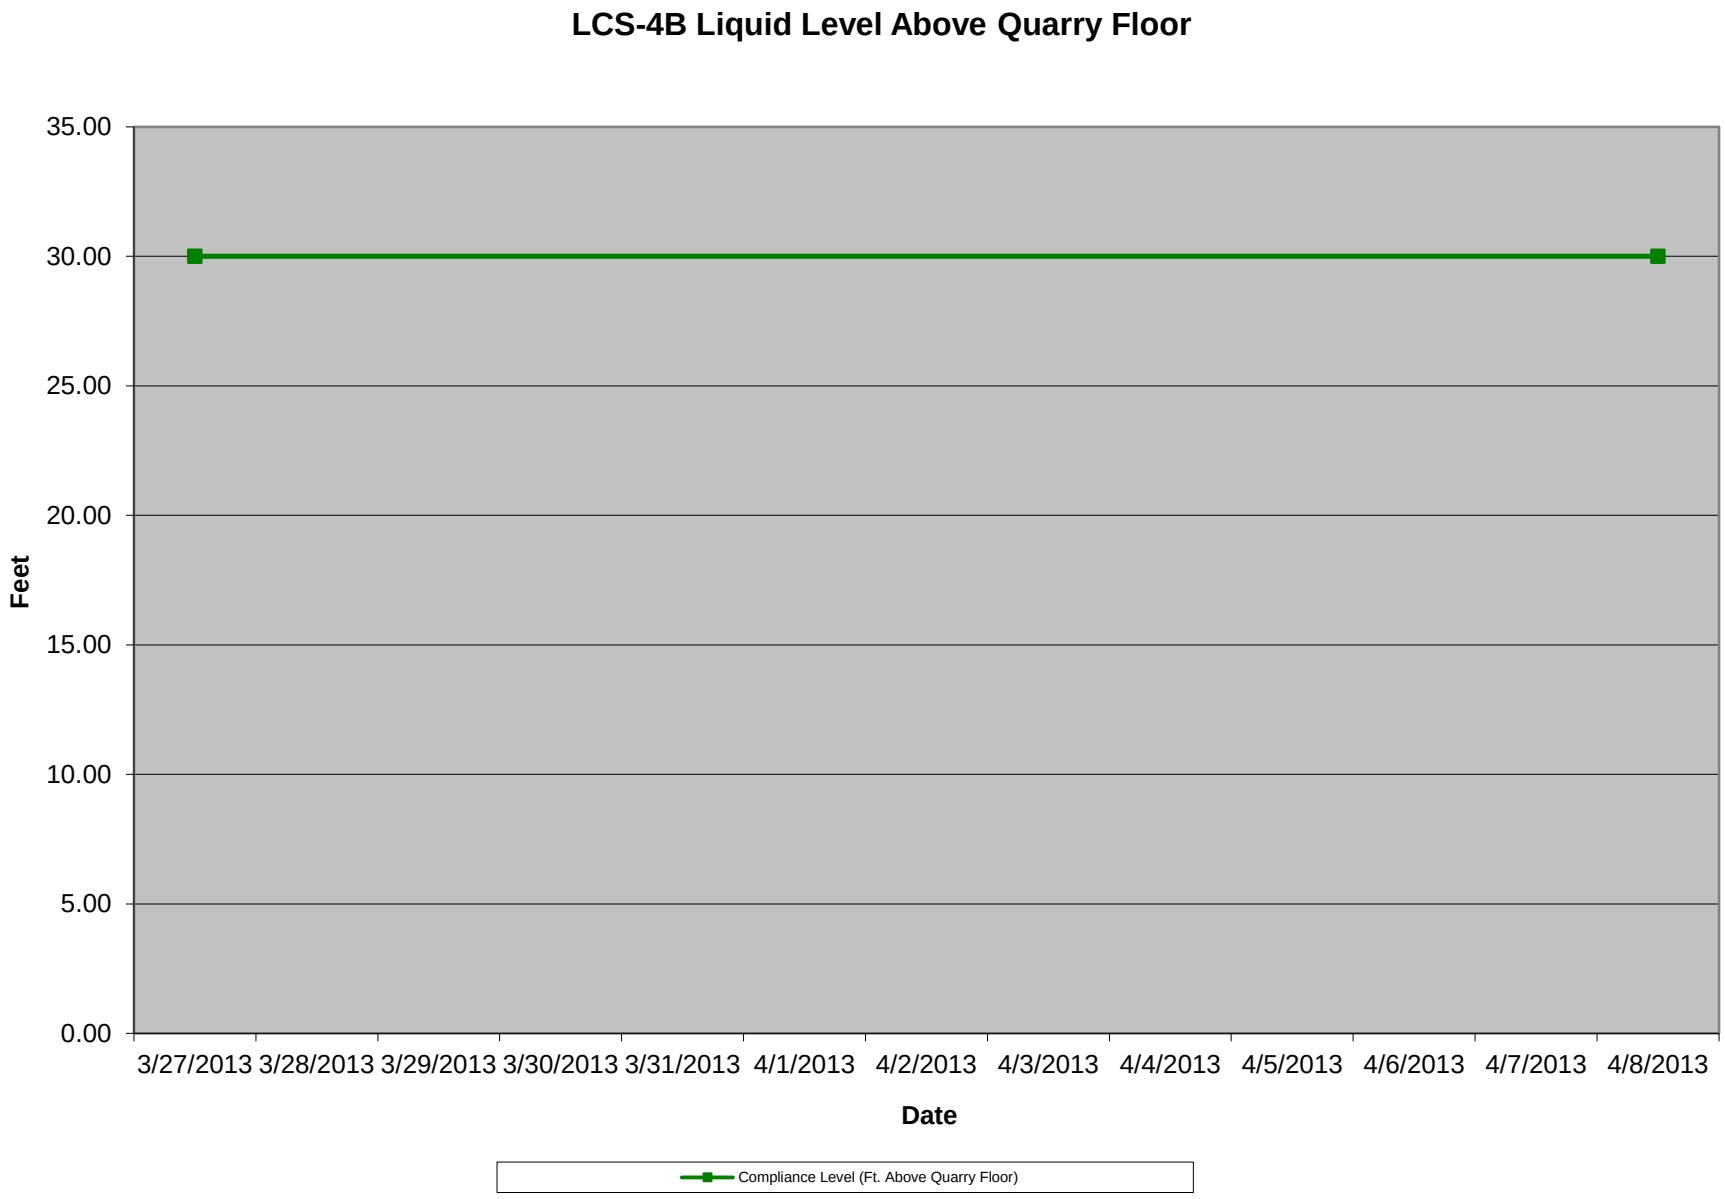
LCS-4B Liquid Level Above Quarry Floor
35.00
30.00
25.00
20.00
15.00
10.00
5.00
0.00
Feet
3/27/2013
3/28/2013
3/29/2013
3/30/2013
3/31/2013
4/1/2013
4/2/2013
4/3/2013
4/4/2013
4/5/2013
4/6/2013
4/7/2013
4/8/2013
Date
Compliance Level (Ft. Above Quarry Floor)

LCS Number	Date Reading Collected	Measured Liquid Level Above Transducer (Ft.)	Transducer Height above Floor of Quarry (Ft.)	Base of Sump Elevation (Ft. MSL)	Height of Liquid (Ft.)	Elevation of Leachate (Ft. MSL)	Compliance Level (Ft. Above Quarry Floor)	Pump on during measurement? (Y/N)	Technician initials	Liquid level meter used	Comments
LCS- 5A	3/27/13	25.9	15.0	235.4	40.9	276.30	50.00	Y	Herst - J. Wilkinson	Dedicated Transducer	
LCS- 5A	4/8/13	41.8	15.0	235.4	56.8	292.20	50.00	N	B. Sehie	Dedicated Transducer	Storage Restriction - Pump Off
LCS- 5A	4/15/13	10.0	15.0	235.4	25.0	260.40	50.00	Y	Herst - M. Stewart	Dedicated Transducer	
LCS- 5A	4/22/13	10.1	15.0	235.4	25.1	260.50	50.00	Y	B. Sehie	Dedicated Transducer	
LCS- 5A	4/29/13	10.1	15.0	235.4	25.1	260.50	50.00	Y	B. Sehie	Dedicated Transducer	
LCS- 5A	5/6/13	10.0	15.0	235.4	25.0	260.40	50.00	Y	Herst - M. Stewart	Dedicated Transducer	
LCS- 5A	5/13/13	10.0	15.0	235.4	25.0	260.40	50.00	Y	B. Sehie	Dedicated Transducer	
LCS- 5A	5/20/13	10.1	15.0	235.4	25.1	260.50	50.00	Y	B. Sehie	Dedicated Transducer	
LCS- 5A	5/27/13	10.1	15.0	235.4	25.1	260.50	50.00	Y	B. Sehie	Dedicated Transducer	
LCS- 5A	6/3/13	14.1	15.0	235.4	29.1	264.50	50.00	Y	B. Sehie	Dedicated Transducer	
LCS- 5A	6/10/13	10.0	15.0	235.4	25.0	260.40	50.00	Y	B. Sehie	Dedicated Transducer	
LCS- 5A	6/17/13	10.1	15.0	235.4	25.1	260.50	50.00	Y	Herst - M. Stewart	Dedicated Transducer	
LCS- 5A	6/24/13	11.9	15.0	235.4	26.9	262.30	50.00	Y	B. Sehie	Dedicated Transducer	

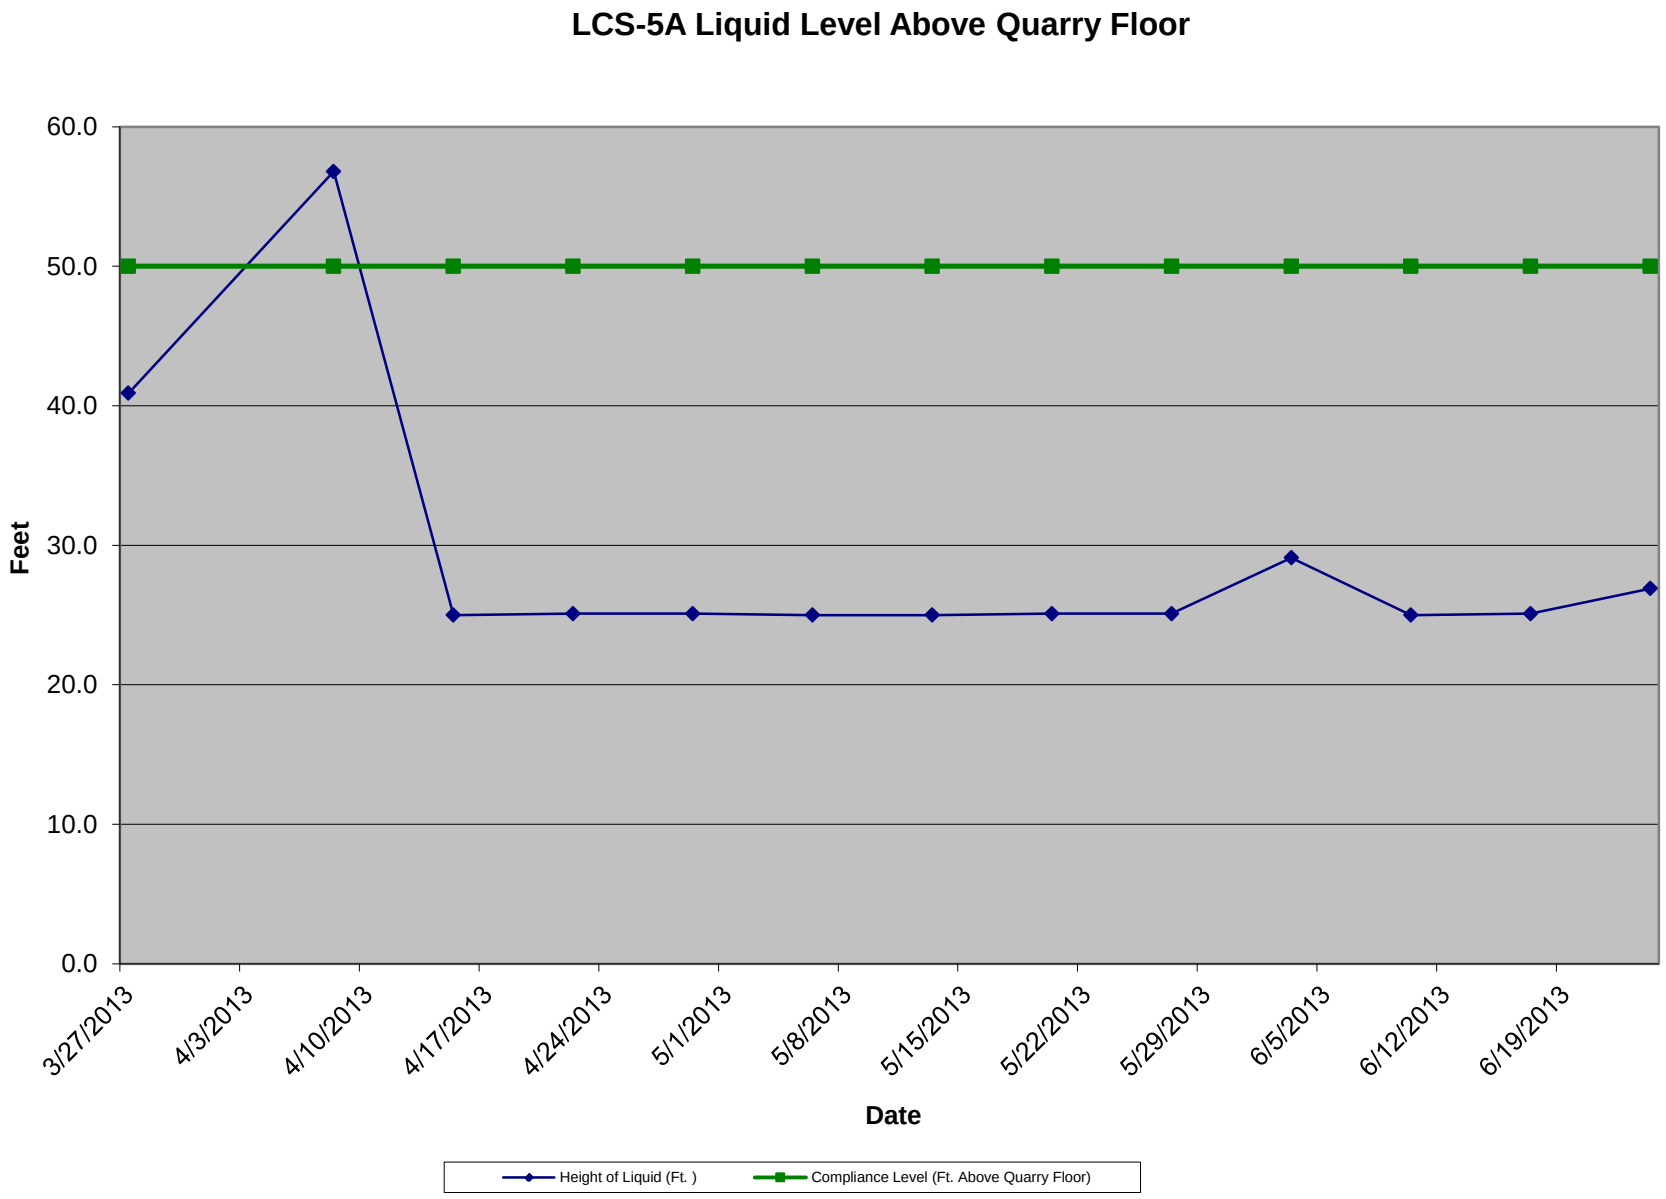
LCS-5A Liquid Level Above Quarry Floor
60.0
50.0
40.0
30.0
20.0
10.0
0.0
Feet
3/27/2013
4/3/2013
4/10/2013
4/17/2013
4/24/2013
5/1/2013
5/8/2013
5/15/2013
5/22/2013
5/29/2013
6/5/2013
6/12/2013
6/19/2013
Date
Height of Liquid (Ft.)
Compliance Level (Ft. Above Quarry Floor)

LCS Number	Date Reading Collected	Measured Liquid Level Above Transducer (Ft.)	Transducer Height above Floor of Quarry (Ft.)	Base of Sump Elevation (Ft. MSL)	Height of Liquid (Ft.)	Elevation of Leachate (Ft. MSL)	Compliance Level (Ft. Above Quarry Floor)	Pump on during measurement? (Y/N)	Technician initials	Liquid level meter used	Comments
LCS- 6B	3/27/13	7.2	9.4	428.52	16.6	445.12	50.00	Y	Herst - J. Wilkinson	Dedicated Transducer	
LCS- 6B	4/8/13	7.3	9.4	428.52	16.7	445.22	50.00	Y	B. Sehie	Dedicated Transducer	Pump in Dry Run Protection Mode (off)
LCS- 6B	4/15/13	9.3	9.4	428.52	18.7	447.22	50.00	Y	Herst - M. Stewart	Dedicated Transducer	
LCS- 6B	4/22/13	10.6	9.4	428.52	20.0	448.52	50.00	Y	B. Sehie	Dedicated Transducer	
LCS- 6B	4/29/13	10.5	9.4	428.52	19.9	448.42	50.00	Y	B. Sehie	Dedicated Transducer	
LCS- 6B	5/6/13	10.6	9.4	428.52	20.0	448.52	50.00	Y	Herst - M. Stewart	Dedicated Transducer	
LCS- 6B	5/13/13	8.4	9.4	428.52	17.8	446.32	50.00	Y	B. Sehie	Dedicated Transducer	
LCS- 6B	5/20/13	10.6	9.4	428.52	20.0	448.52	50.00	Y	B. Sehie	Dedicated Transducer	
LCS- 6B	5/27/13	9.6	9.4	428.52	19.0	447.52	50.00	Y	B. Sehie	Dedicated Transducer	
LCS- 6B	6/3/13	9.1	9.4	428.52	18.5	447.02	50.00	Y	B. Sehie	Dedicated Transducer	
LCS- 6B	6/10/13	11.1	9.4	428.52	20.5	449.02	50.00	Y	B. Sehie	Dedicated Transducer	
LCS- 6B	6/17/13	11.0	9.4	428.52	20.4	448.92	50.00	Y	Herst - M. Stewart	Dedicated Transducer	
LCS- 6B	6/24/13	11.1	9.4	428.52	20.5	449.02	50.00	Y	B. Sehie	Dedicated Transducer	

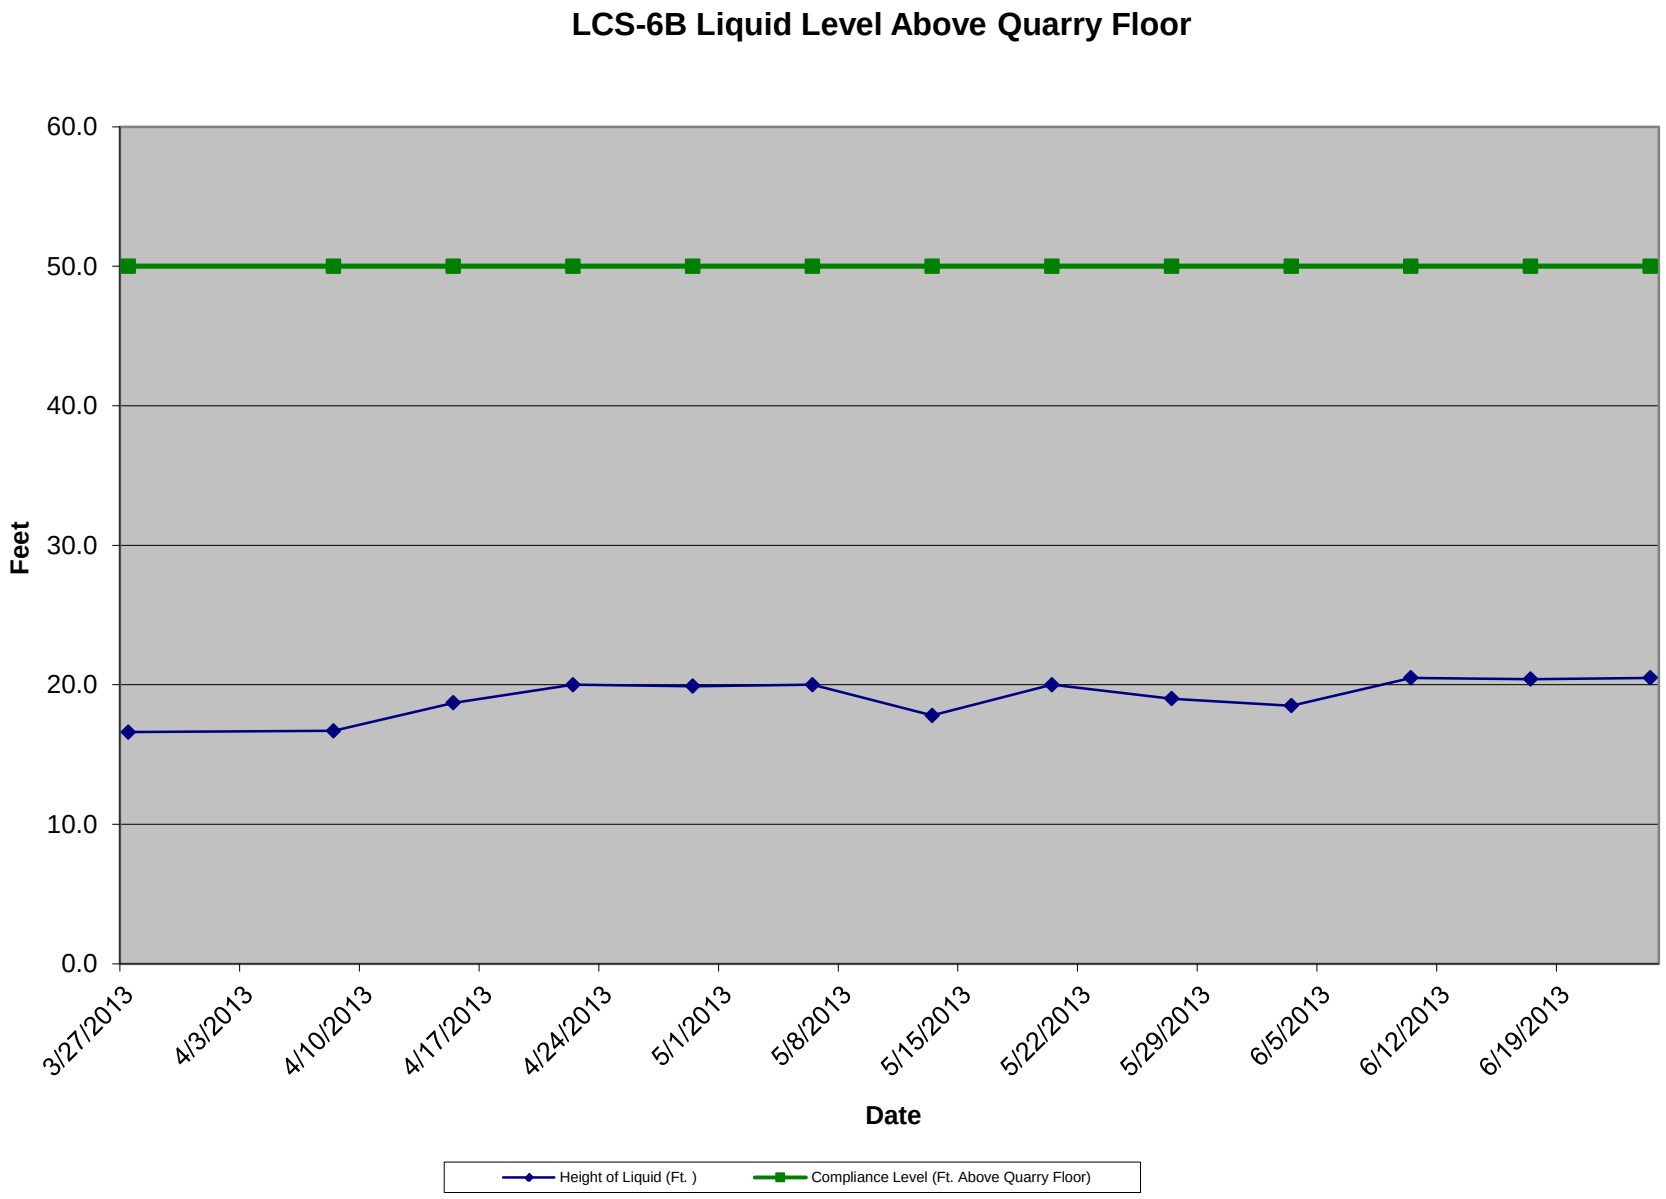
LCS-6B Liquid Level Above Quarry Floor
60.0
50.0
40.0
30.0
20.0
10.0
0.0
Feet
3/27/2013
4/3/2013
4/10/2013
4/17/2013
4/24/2013
5/1/2013
5/8/2013
5/15/2013
5/22/2013
5/29/2013
6/5/2013
6/12/2013
6/19/2013
Date
Height of Liquid (Ft.)
Compliance Level (Ft. Above Quarry Floor)
