JAMES E. GRIBI

1700 KSB & L BLDG.
WICHITA, KANSAS

OPERATOR	EARTH REFERENCE SYSTEMS
WELL NO.	1
LEASE	SHAWN
LOCATION	2W-NE-NE
COUNTY	KNOX
ELEV.	980 KB
SEC.	10
TWP.	62
RGE.	13
CONTRACTOR	EAR DRILLING
SPUD DATE	8-1-89
COMPL. DATE	8-7-89
TOTAL DEPTH	1101 RTD
CASING RECORD	8-5/8" @ 25'
PRODUCTION	DRY & ABANDONED
FIELD	WILDCAT
DRILL STEM TEST	NONE
CORES	NONE
ELECTRICAL LOGS	SCHLUMBERGER DIL/SONIC/FDC/CNL
DRILLER	JOHN GARDY
GEOLOGIST	DAVID A.

DAILY PENETRATION

DATE	DEPTH	REMARKS
7-31-89	0	MOVE IN & RIGGED UP. SPUDDED 12:00
8-1-89	0	WOB 20, RPM 60, GPM 60, PUMP PRESS 1200
8-2-89	340	
8-3-89	640	
8-4-89	940	
8-5-89	1101	RTD 1101, R.U. SCHLUM. RUN DIL, SONIC, FDC, CNL

DRILL STEM TESTS

NO.	PERIODS	BOT. TIME	CUSHION TYPE	CUSHION TIME	BHP	BHT	RECOVERY
NONE							

BIT RECORD

NO.	SIZE	MAKE	TYPE	DEPTH OUT	FEET	HOURS	DULL
1	12-1/4	SMITH	F-31	115	115	4-1/2	
2	7-7/8	SMITH	F-31	1101	986	34-1/2	
3	7-7/8	SMITH	F-31	1101	986	41-1/2	

MUD RECORD

FILL MUD PIT

NO.	DEPTH	WT.	VIS.	PV.	YP.	GEL.	PH.	CHL.	REMARKS
1	34	8.4	35	13.0	5.7	4	9.0	300	—
2	425	8.7	35	12.4	9.7	4	9.1	300	—
3	755	8.4	44	9.7	14.7	2	9.5	300	—
4	846	8.4	34	9.4	12.7	2	9.0	300	—

LEGEND

SHALE, LIMESTONE, DOLOMITE, CHERT, SANDSTONE, SHALE, LIMESTONE, DOLOMITE, CHERT, SANDSTONE

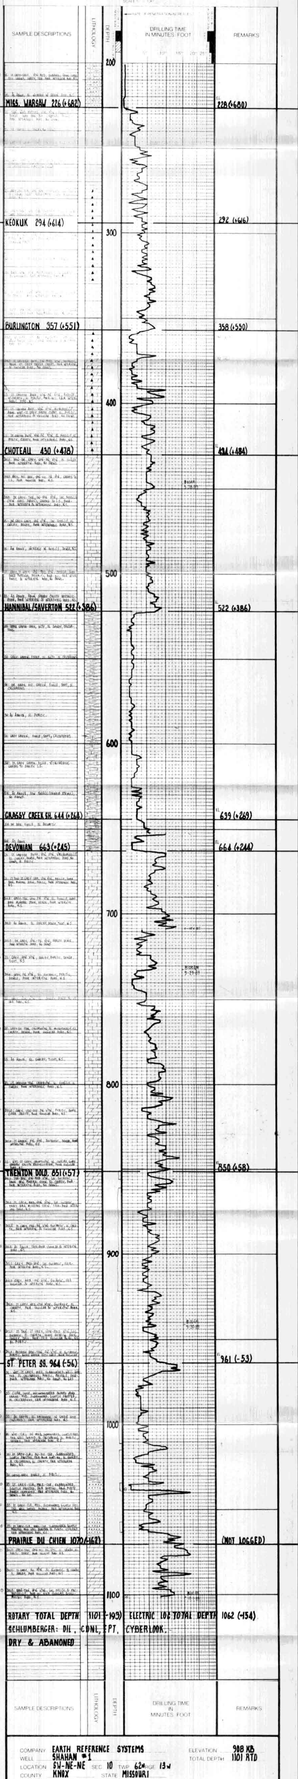

COMPANY	EARTH REFERENCE SYSTEMS	ELEVATION	980 KB
WELL	SHAWN #1	TOTAL DEPTH	1101 RTD
LOCATION	2W-NE-NE SEC. 10 TWP. 62 RGE. 13		
COUNTY	KNOX STATE MISSOURI		

DRILL STEM TESTS - CORES - REMARKS

REMARKS & RECOMMENDATIONS

BASED ON THE INFORMATION ON HAND, THE WELL HAS BEEN PLUGGED AS FOLLOWS: 40 SACKS CEMENT AT 1100', 40 SACKS CEMENT AT 25', 10 SACKS CEMENT IN RATHOLE AND MOUSEHOLE. SURFACE PIPE WAS PULLED AND CEMENTED.

I RECOMMEND THAT THIS WELL BE PLUGGED AND ABANDONED.

RESPECTFULLY SUBMITTED,
JAMES E. GRIBI
