Tucker WIRELINE SERVICES

Released until 8-11-10

~~CONFIDENTIAL~~ # 22399

COMPENSATED NEUTRON PEL DENSITY LOG

RECEIVED AUG 11 2009 Mo Oil & Gas Council

File No. : TUL-55420
Company : RUNNING FOXES PETROLEUM
Well : STONER #14-6B-2
Field :
County : VERNON
State : MISSOURI
Country : U.S.A.

Location : PERMIT # 22399 1140' FSL & 1530' FWL

Sect : 06 Twp : 36N Rge : 33W

Recorded By : R. FRANKLIN
Witnessed By : M. MACHOSKY

Date : MAR 26 2009
Run No. : 1

Permanent Datum : GL
Drilling Measured From : GL
Log Measured From : GL
Above Permanent Datum : 0.00 FT

Elevations :
KB :
DF :
GL : 877.00 FT

Additional Services
PIT

The customer is hereby warned that by providing the log data herein, T. W. S. does not agree to provide any interpretation of log data, conversion of log data to physical rock parameters or recommendations. T. W. S. does not guarantee or warrant either expressly or impliedly, the accuracy of any interpretation of log data, conversion of log data to physical rock parameters or recommendations which may be given by T. W. S. personnel. Any interpretation, conversion or recommendation is not part of the consideration for the agreement between the parties and is not part of any part of the charge by T. W. S. for its services. Any user of the log data is warned that said user is not entitled to rely on intepretations, conversions or recommendations as aforesaid.

Run Number 1

Depth To Fluid	0.0	FT		
Fluid Type In Hole :	NATIVE			
Density :	0.000	LBS/GAL		
Viscosity :	0.000	SEC		
pH :	0.000			
Fluid Loss :	0.000	CC		
Salinity :	0.000			
RM Source :	MEASURED			
RM :	1.200	OHMM at	65	F
RM at BHT :	1.090	OHMM at	72	F
RMF Source :	CALCULATED			
RMF :	1.020	OHMM at	65	F
RMF at BHT :	0.930	OHMM at	72	F
RMC Source :	CALCULATED			
RMC :	1.380	OHMM at	65	F
RMC at BHT :	1.250	OHMM at	72	F
Max Recorded Temp. :			72	F
Time Circulation Stopped :				
Operating Rig Time, Hrs. :			2.0	

- Source Serial Numbers -

Gamma	2991GW
Neutron	N-1046

Sonde Serial Numbers

GRTB	GRT-BC-41
CNT	CNP-AE-42
LDT	LDP-CA-06
PIT_B	PIT-AB-005

Casing Strings

Size (IN)	Weight (LBS)	Bottom (FT)
.000	15.00	21.00

- Comments -

ALL PRESENTATIONS AS PER CUSTOMER REQUEST.

GRT, CNT, LDT, AND PIT RUN IN COMBINATION.
2.71 G/CC USED TO CALCULATE POROSITY.
ANNULAR HOLE VOLUME CALCULATED USING 4.5" PRODUCTION CASING.
PHIN IS CALIPER CORRECTED.

OPERATORS:
M. GARNER
S. DAVIS

THANK YOU FOR USING TUCKER WIRELINE!!!

Tool String Schematic

Total Tool Length 43.49 ft.
Maximum Outside diameter 4.00 in.
Net Weight in Air 243.00 lbs.

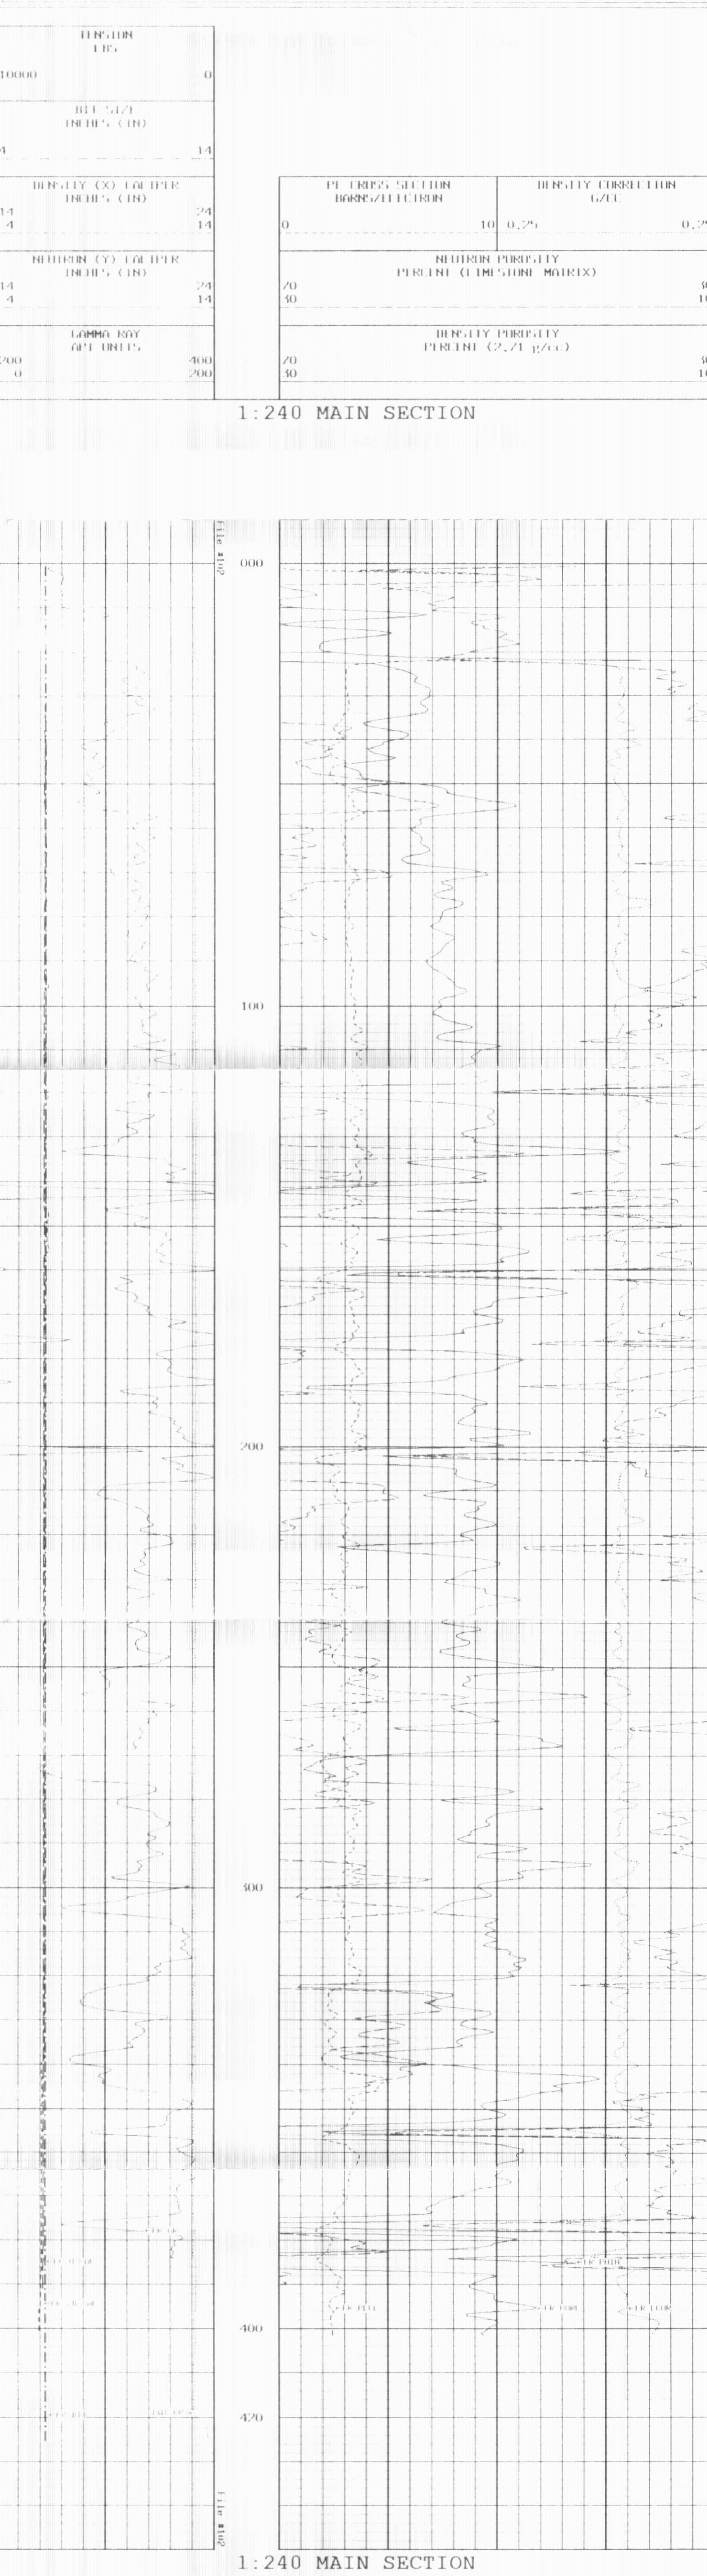

1:240 MAIN SECTION

1:240 REPEAT SECTION

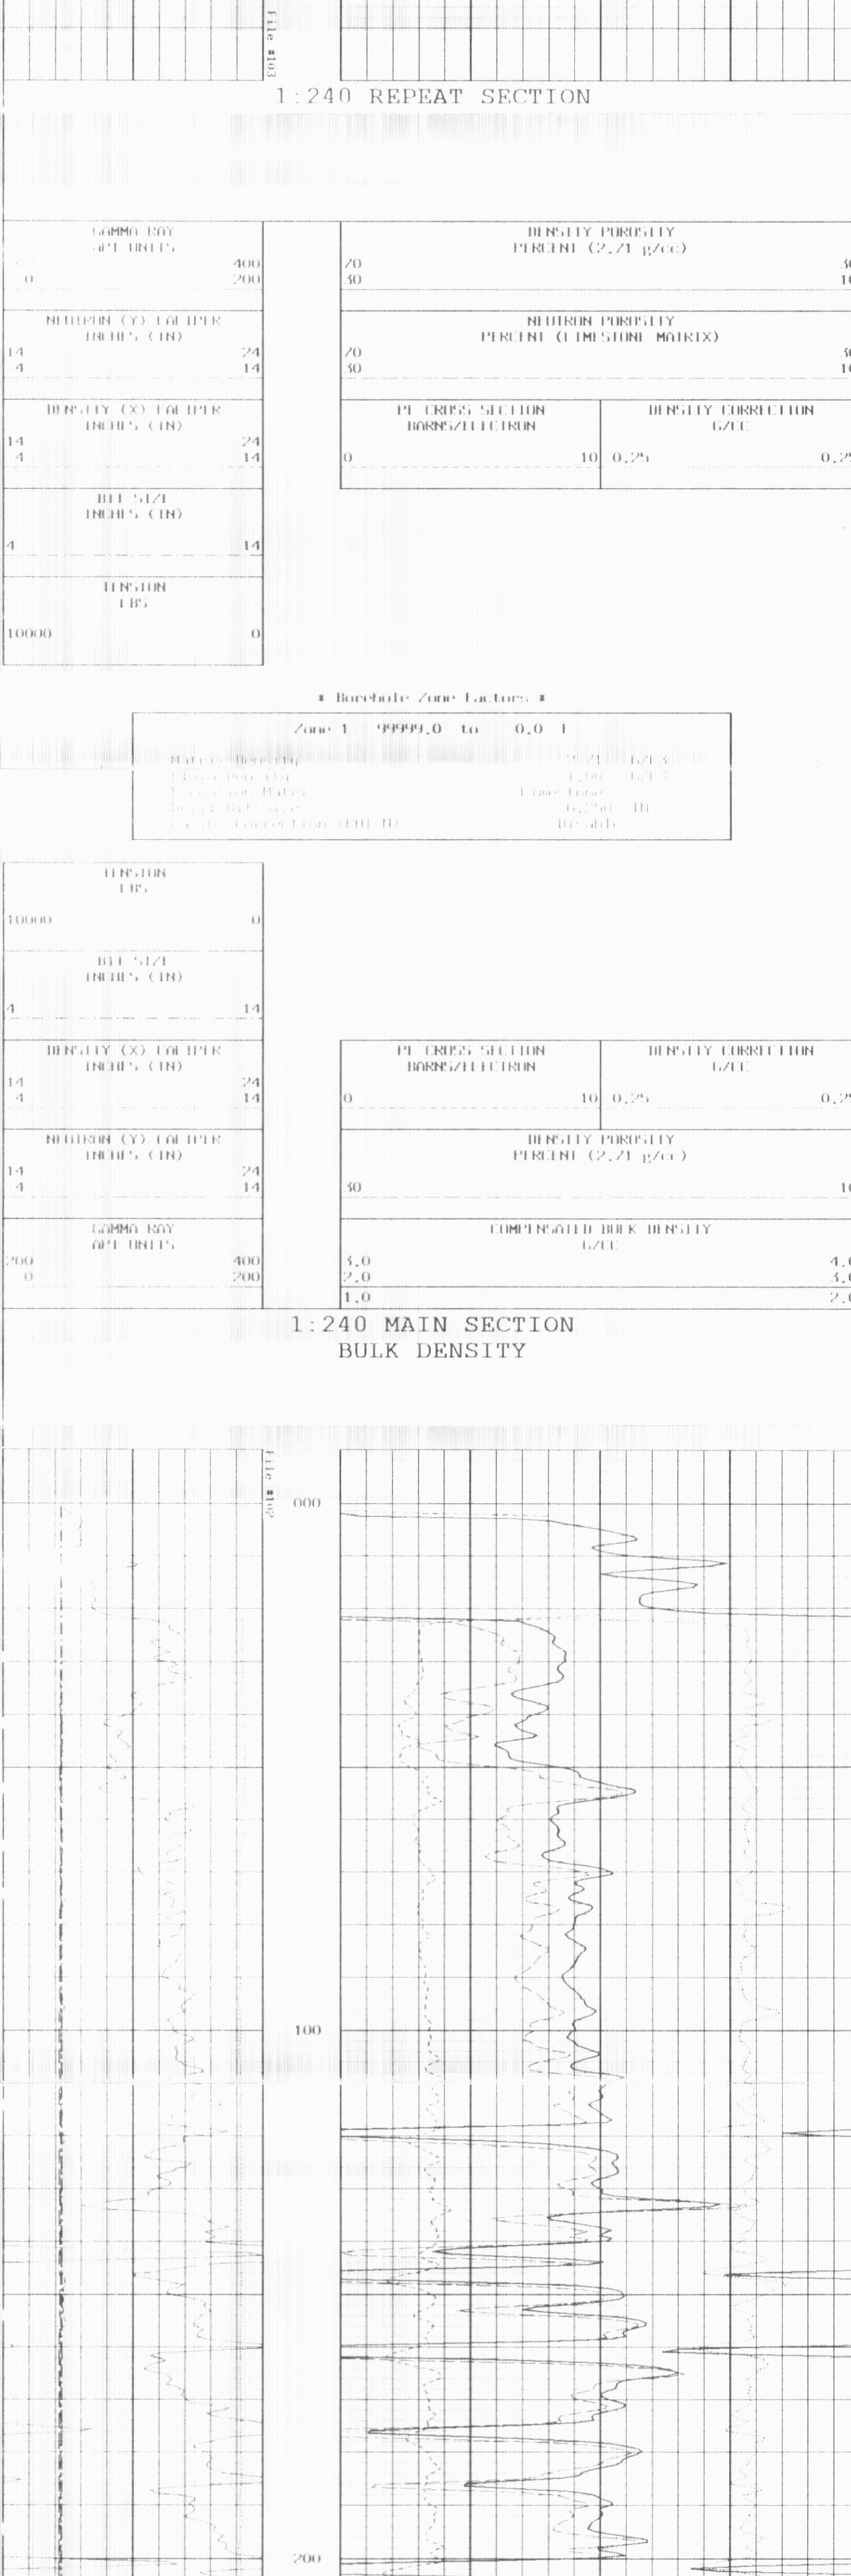

1:240 MAIN SECTION
BULK DENSITY
