Tucker WIRELINE SERVICES

COMPENSATED NEUTRON PEL DENSITY LOG

CONFIDENTIAL

RECEIVED NOV 22 2010 Mo Oil & Gas Council

File No. : TUL-54766
Company : RUNNING FOXES PETROLEUM, LLC
Well : STONER 4-7B-2A
Field :
County : VERNON
State : MISSOURI
Country : USA

Location : PERMIT#: 22599
5' FNL & 210' FWL

Sect : 7 Twp : 36N Rge : 33W

Recorded By : B.BAILEY
Witnessed By : C.COUNTS

Date : OCT 5 2010
Run No. : 0

Elevations :

Additional Services
PIT

The customer is hereby warned that by providing the log data herein, T. W. S. does not agree to provide any interpretation of log data, conversion of log data to physical rock parameters or recommendations. T. W. S. does not guarantee or warrant either expressly or impliedly, the accuracy of any interpretation of log data, conversion of log data to physical rock parameters or recommendations which may be given by T. W. S. personnel. Any interpretation, conversion or recommendation is not part of the consideration for the agreement between the parties and is not part of any part of the charge by T. W. S. for its services. Any user of the log data is warned that said user is not entitled to rely on intepretations, conversions or recommendations as aforesaid.

Run Number 0

Depth To Fluid	0.0	FT		
Fluid Type in Hole :	NATIVE			
Density :	0.000	SG		
Viscosity :	0.000	SEC		
pH :	0.000			
Fluid Loss :	7.400			
Salinity :	0.000	KPPM		
RM Source :	MEASURED			
RM :	10.000	OHMM at	72	F
RM at BHT :	10.000	OHMM at	72	F
RMF Source :	CALCULATED			
RMF :	8.500	OHMM at	72	F
RMF at BHT :	8.500	OHMM at	72	F
RMC Source :	CALCULATED			
RMC :	11.500	OHMM at	72	F
RMC at BHT :	11.500	OHMM at	72	F
Max Recorded Temp. :			72	F
Time Circulation Stopped :				
Operating Rig Time, Hrs. :			1.0	

- Source Serial Numbers -

Gamma	CSV-587
Neutron	N-1044

- Sonde Serial Numbers -

GRTB	GRT-BA-14
CNT	CNP-AA-111
LDTNG	LDP-NG-02
PIT	PIT-AB-14

Casing Strings

Size (IN)	Weight (LB/FT)	Bottom (FT)
7.000	32.00	20.00

- Comments -

ALL PRESENTATIONS AS PER CUSTOMER REQUEST.

GRT, CNT, LDT, PIT RAN IN COMBINATION
CALIPERS ORIENTED ON THE X-Y AXIS.
PHIN IS CALIPER CORRECTED.
ANNULAR HOLE VOLUME CALCULATED USING 4.500" PRODUCTION CASING.

LDT: ..., PEFIN, CLLPIN, LDEMN, PORLLS, PECSN.

Tool String Schematic

Total Tool Length
Maximum Outside diameter
Net Weight in Air

1:240 MAIN SECTION

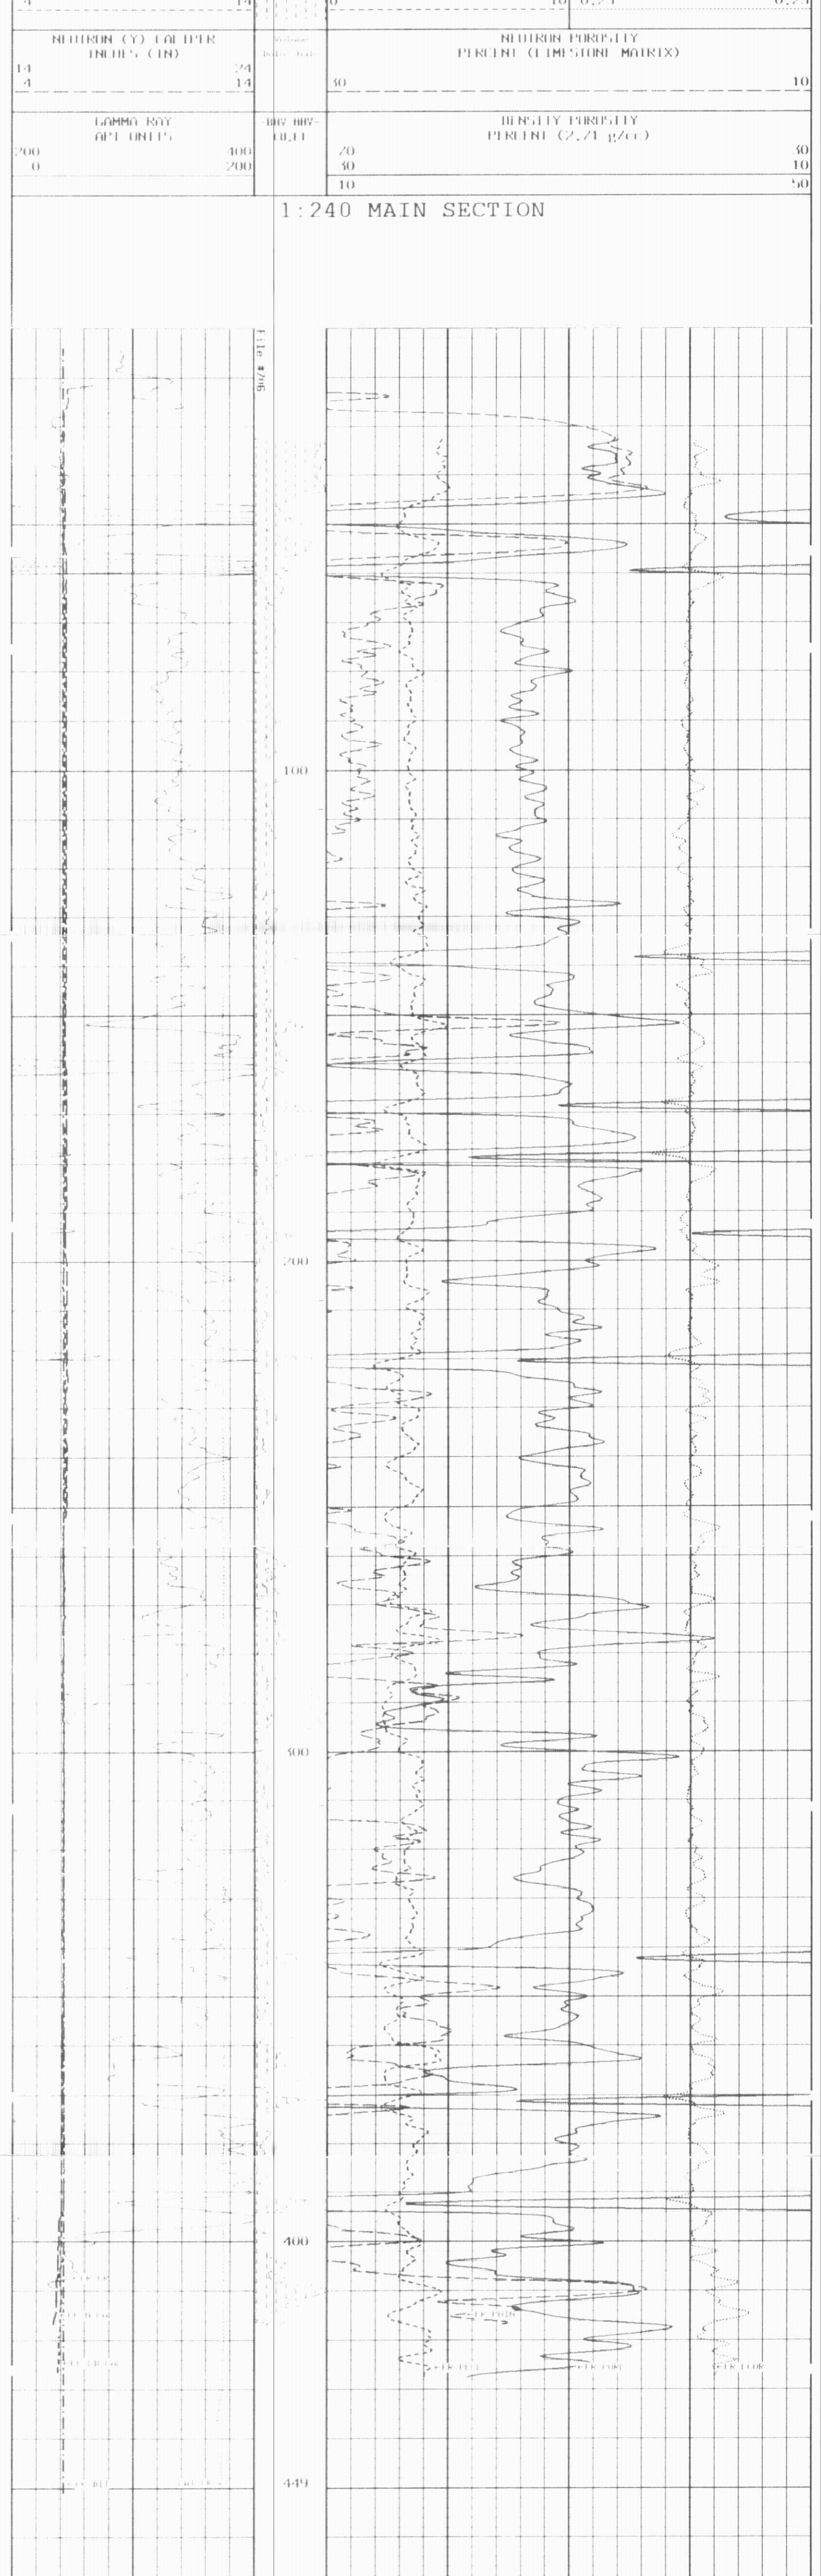

1:240 MAIN SECTION

1:240 REPEAT SECTION

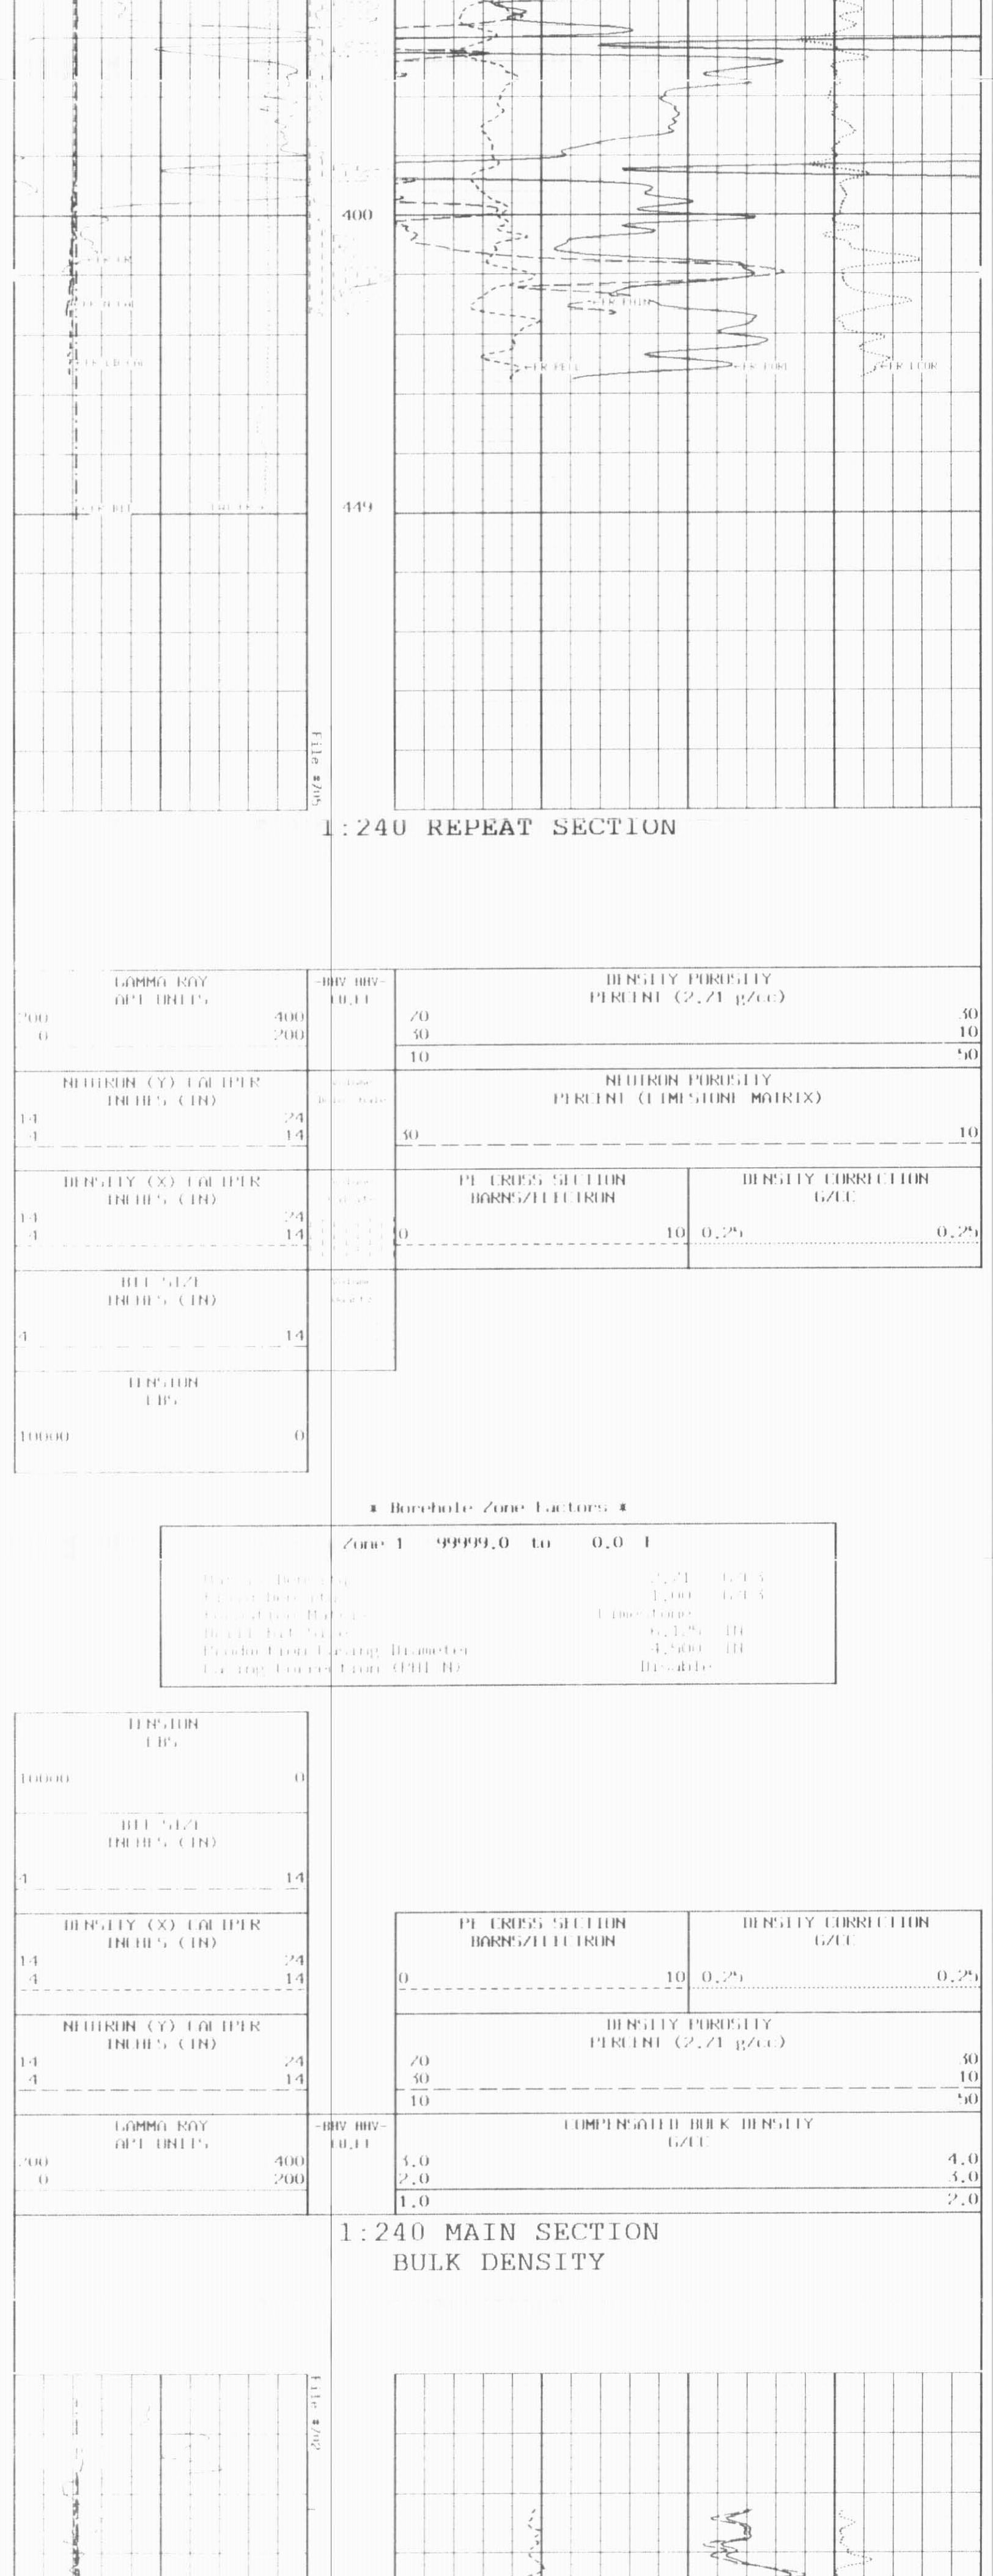

1:240 REPEAT SECTION

1:240 MAIN SECTION
BULK DENSITY

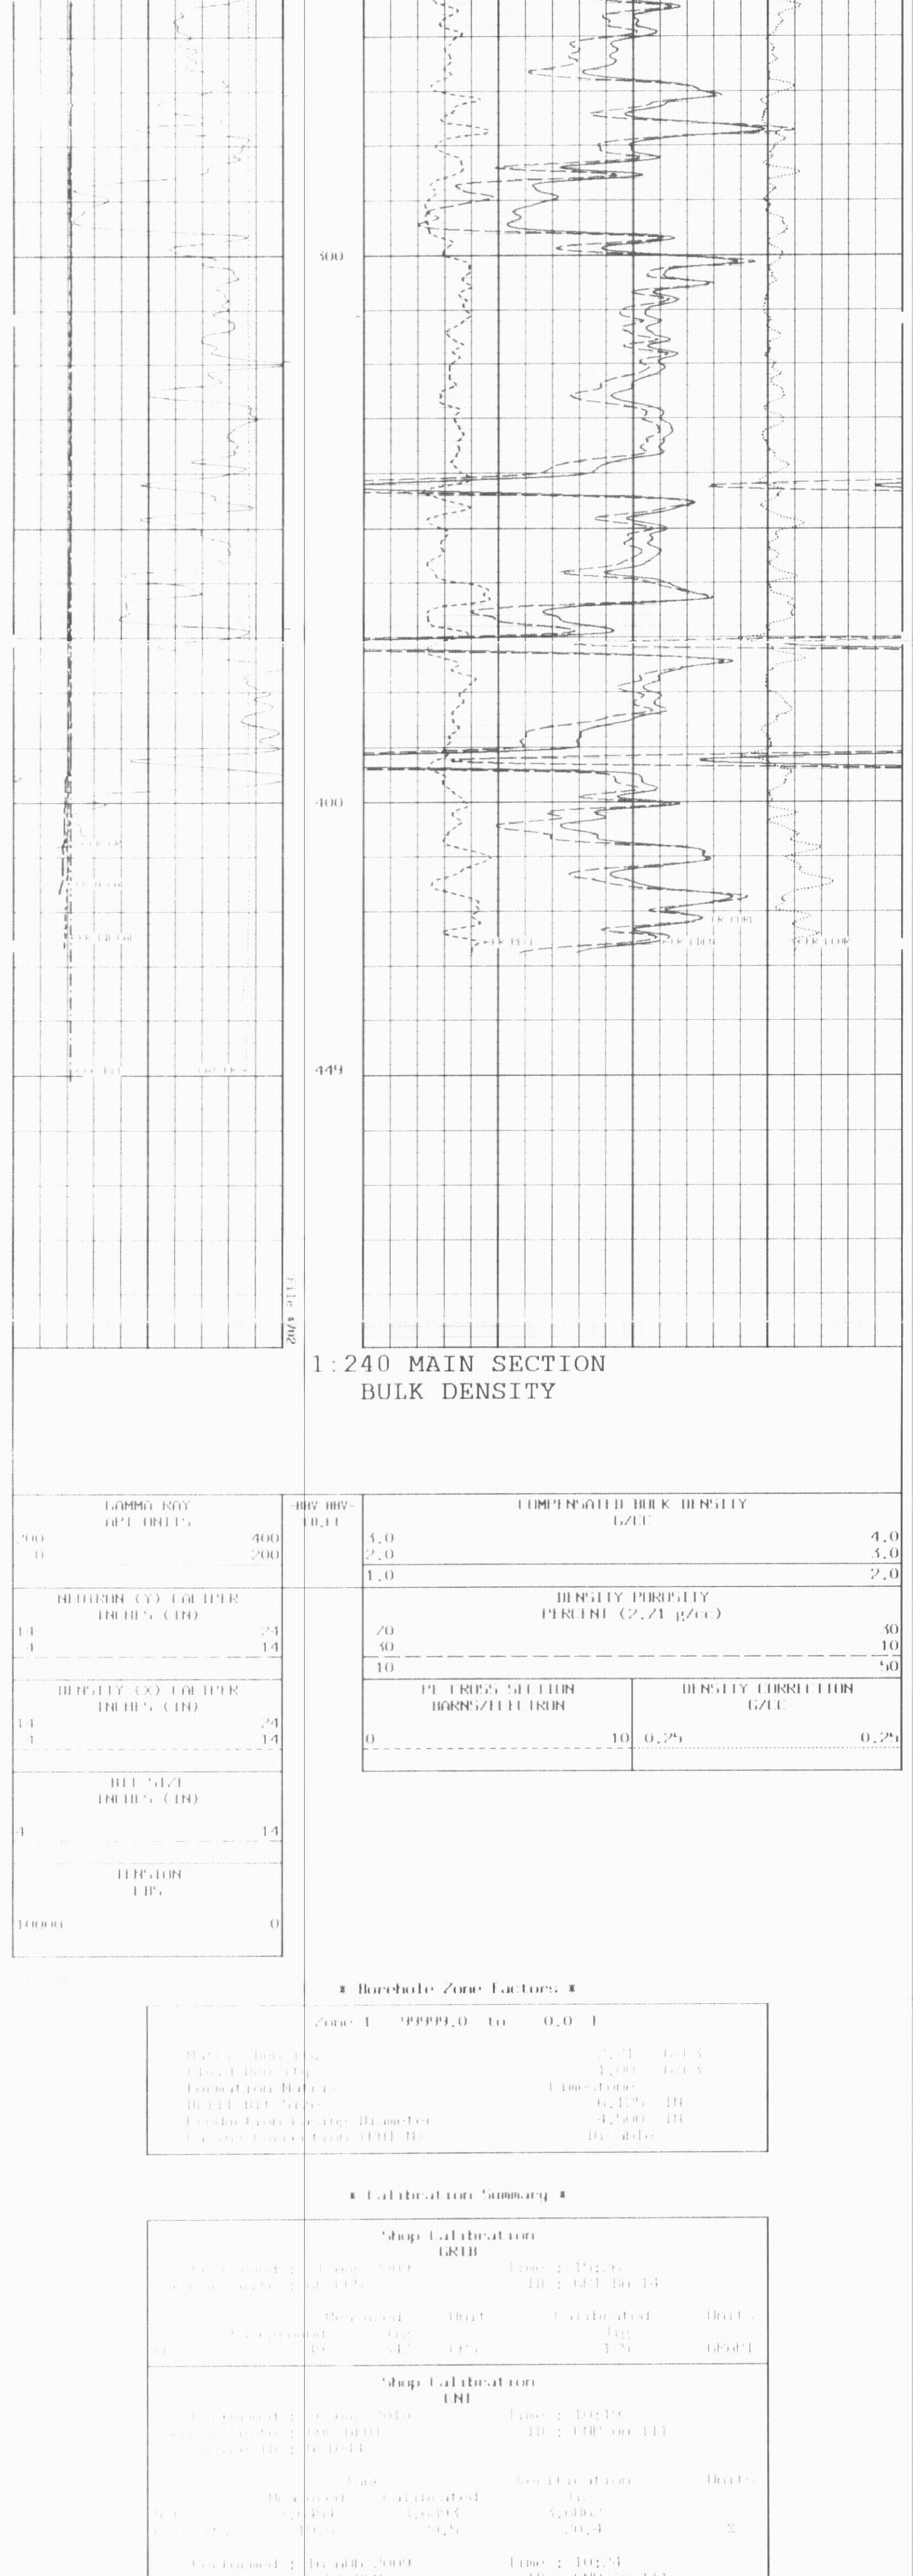

1:240 MAIN SECTION
BULK DENSITY
