217-22086

Tucker WIRELINE SERVICES

COMPENSATED NEUTRON PEL DENSITY LOG

RECEIVED NOV 03 2008 KS Oil & Gas Council

CONFIDENTIAL Released 11/03/2009

File No. : TUL-32877
Company : RUNNING FOXES PETROLEUM, INC.
Well : STONER 6-7A
Field :
County : VERNON
State : MISSOURI
Country : U.S.A.

Location : PERMIT#: 22086 2300' FNL & 2200' FWL

Sect : 07 Twp : 36N Rge : 33W

Recorded By : B.BAILEY
Witnessed By : C.TAGLIERI

Elevations :
KB :
DF :
GL : 877.00 FT

Date : JUN 25 2008
Run No. : 1

Permanent Datum : GL
Drilling Measured From : GL
Log Measured From : GL
Above Permanent Datum : 0.00 FT

Depth--Driller : 402.0 FT
Depth--Logger : 402.0 FT
Bottom Log Interval : 393.0 FT
Top Log Interval : 20.0 FT

Casing Depth--Driller : 22.0 FT
Casing Depth--Logger : 22.0 FT
Casing Diameter : 7.000 IN

Bit Size : 6.250 IN
Unit No. : 118
Location : TULSA

Additional Services
PIT

The customer is hereby warned that by providing the log data herein, T. W. S. does not agree to provide any interpretation of log data, conversion of log data to physical rock parameters or recommendations. T. W. S. does not guarantee or warrant either expressly or impliedly, the accuracy of any interpretation of log data, conversion of log data to physical rock parameters or recommendations which may be given by T. W. S. personnel. Any interpretation, conversion or recommendation is not part of the consideration for the agreement between the parties and is not part of any part of the charge by T. W. S. for its services. Any user of the log data is warned that said user is not entitled to rely on interpretations, conversions or recommendations as aforesaid.

Run Number 1

Depth To Fluid	0.0	FT		
Fluid Type In Hole :	NATIVE/ AIR			
Density :	0.000	LBS/GAL		
Viscosity :	0.000	SEC		
pH :	0.000			
Fluid Loss :	0.000	CC		
Salinity :	0.000			
RM Source :	MEASURED			
RM :	0.000	OHMM at	0	F
RM at BHT :	0.000	OHMM at	86	F
RMF Source :	CALCULATED			
RMF :	0.000	OHMM at	0	F
RMF at BHT :	0.000	OHMM at	86	F
RMC Source :	CALCULATED			
RMC :	0.000	OHMM at	0	F
RMC at BHT :	0.000	OHMM at	86	F
Max Recorded Temp. :			86	F
Time Circulation Stopped :				
Operating Rig Time, Hrs. :			2.5	

- Source Serial Numbers -

Gamma	317-49B
Neutron	21166B

- Sonde Serial Numbers -

GRTB	GRT-BC-41
CNT	CNP_AA_102
LDTNG	LDP-NG-01

Casing Strings

Size (IN)	Weight (LB/FT)	Bottom (FT)
7.000	23.00	22.00

- Comments -

ALL PRESENTATIONS AS PER CUSTOMER REQUEST.

RUN# 1: GRT, PIT.
RUN# 2: GRT, CNT, LDT.
CALIPERS ORIENTED ON THE X-Y AXIS.
PHIN IS CALIPER CORRECTED.
1.5" STANDOFF DEPLOYED ON PIT.
ANNULAR HOLE VOLUME CALCULATED USING 4.50" PRODUCTION CASING.
2.71 G/C USED TO CALCULATE POROSITY.

GRT: GRP.
CNT: PHIN, CLCNIN, PHINLS.
LDT: PORL, LCORN, PECLN, CLDIN, LDENN, PORLLS, PECSN.
PIT: CILD, SPU, ILM, ILD, SFLAEC.

OPERATORS:

R.MCDANIEL
F.FRANKLIN
S.BARTO
THANK YOU FOR USING TUCKER WIRELINE SERVICES!

Tool String Schematic

Total Tool Length [illegible] ft.
Maximum Outside diameter [illegible] in.
Net Weight in Air [illegible] lbs.

1:240 MAIN SECTION

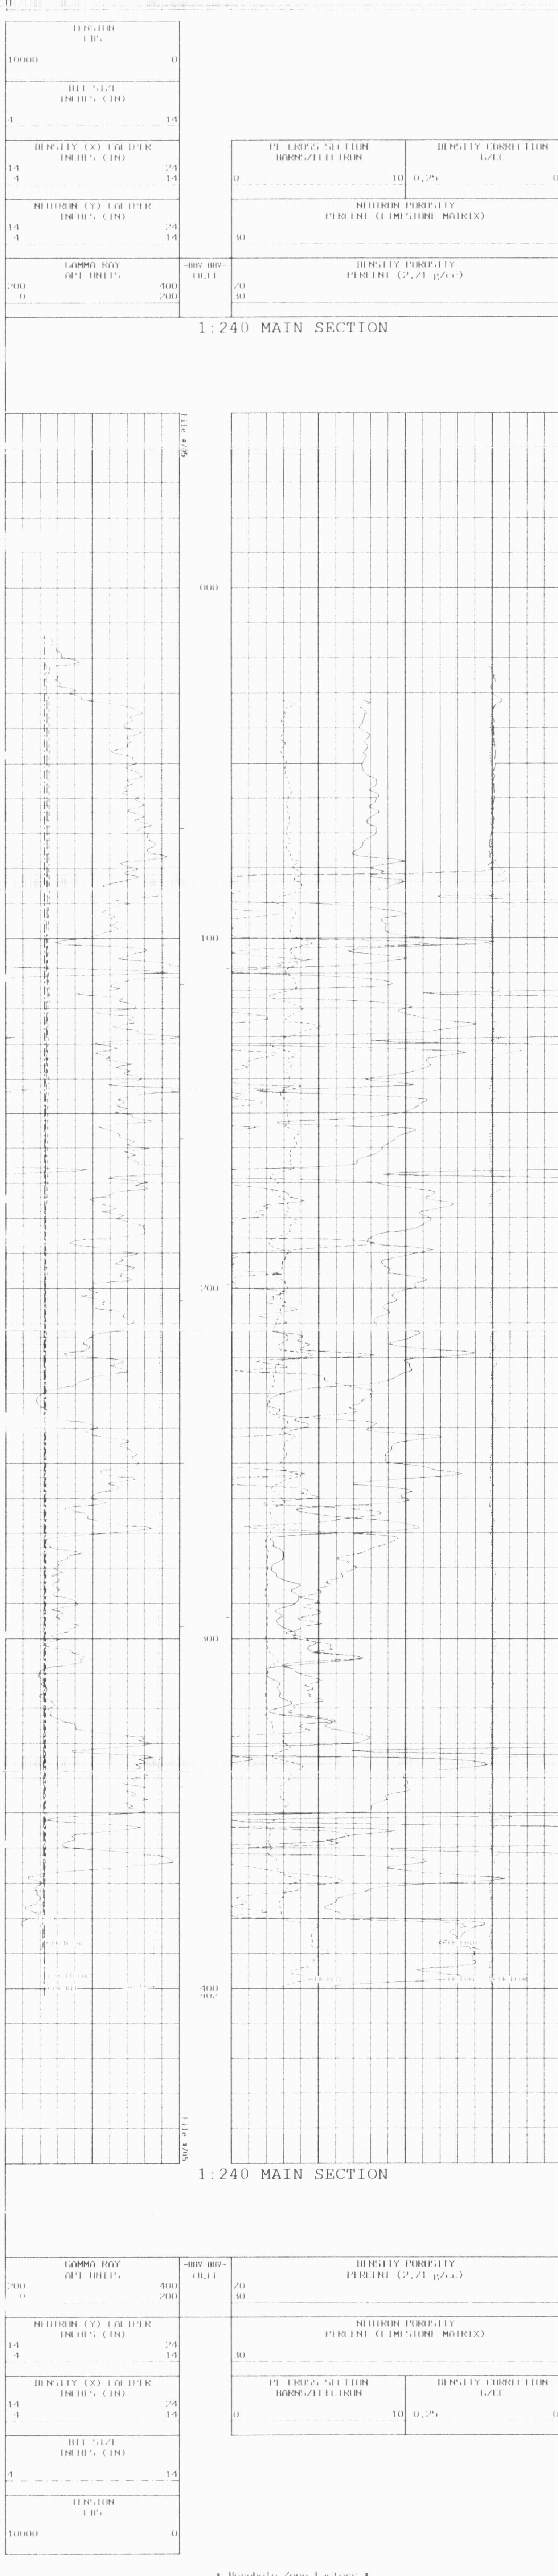

1:240 MAIN SECTION

1:240 REPEAT SECTION

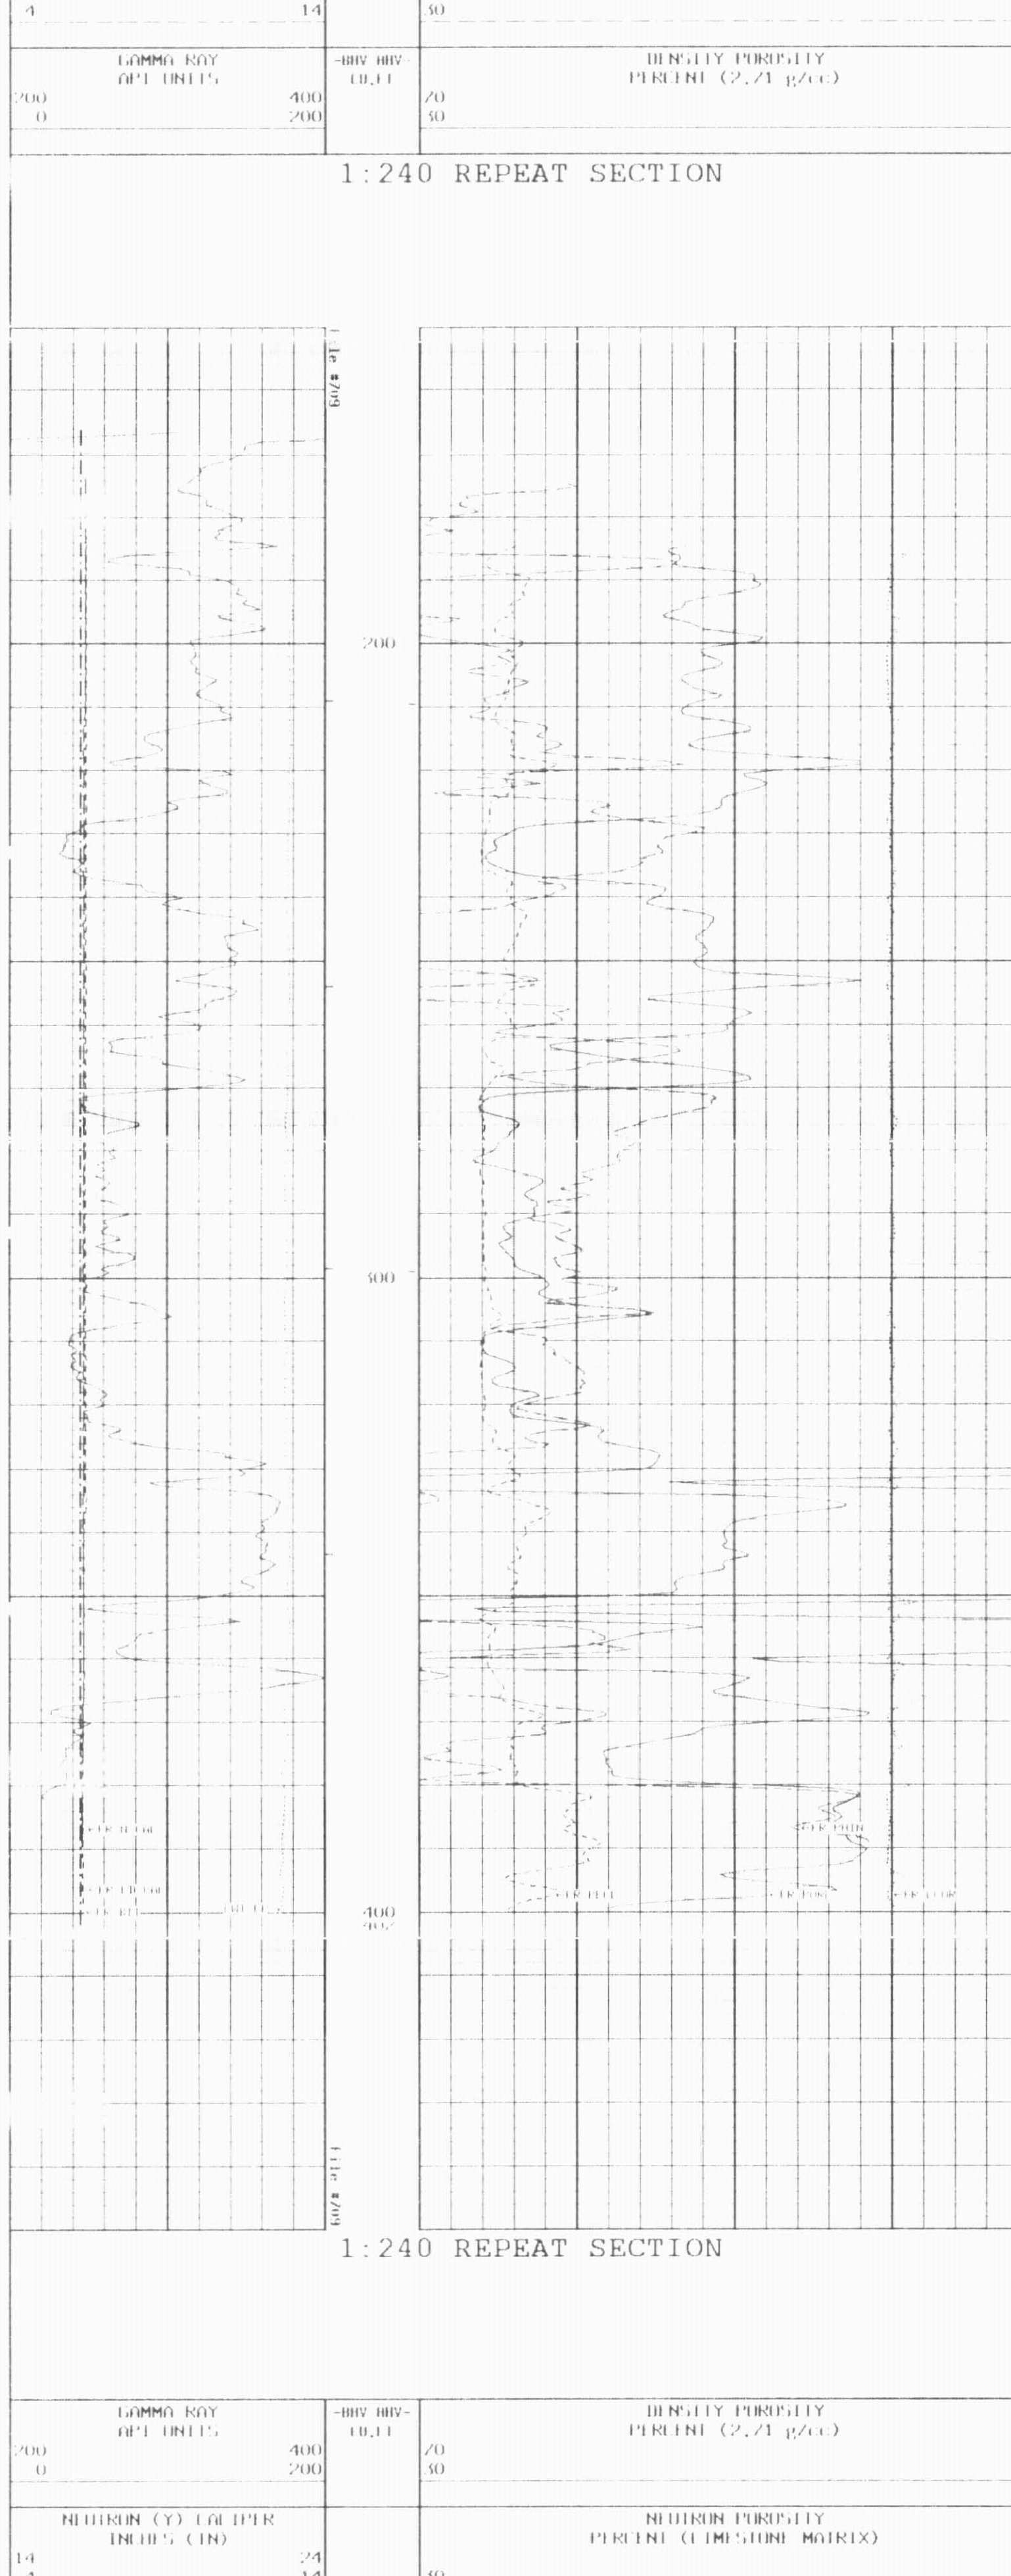

1:240 REPEAT SECTION

1:240 MAIN SECTION
BULK DENSITY

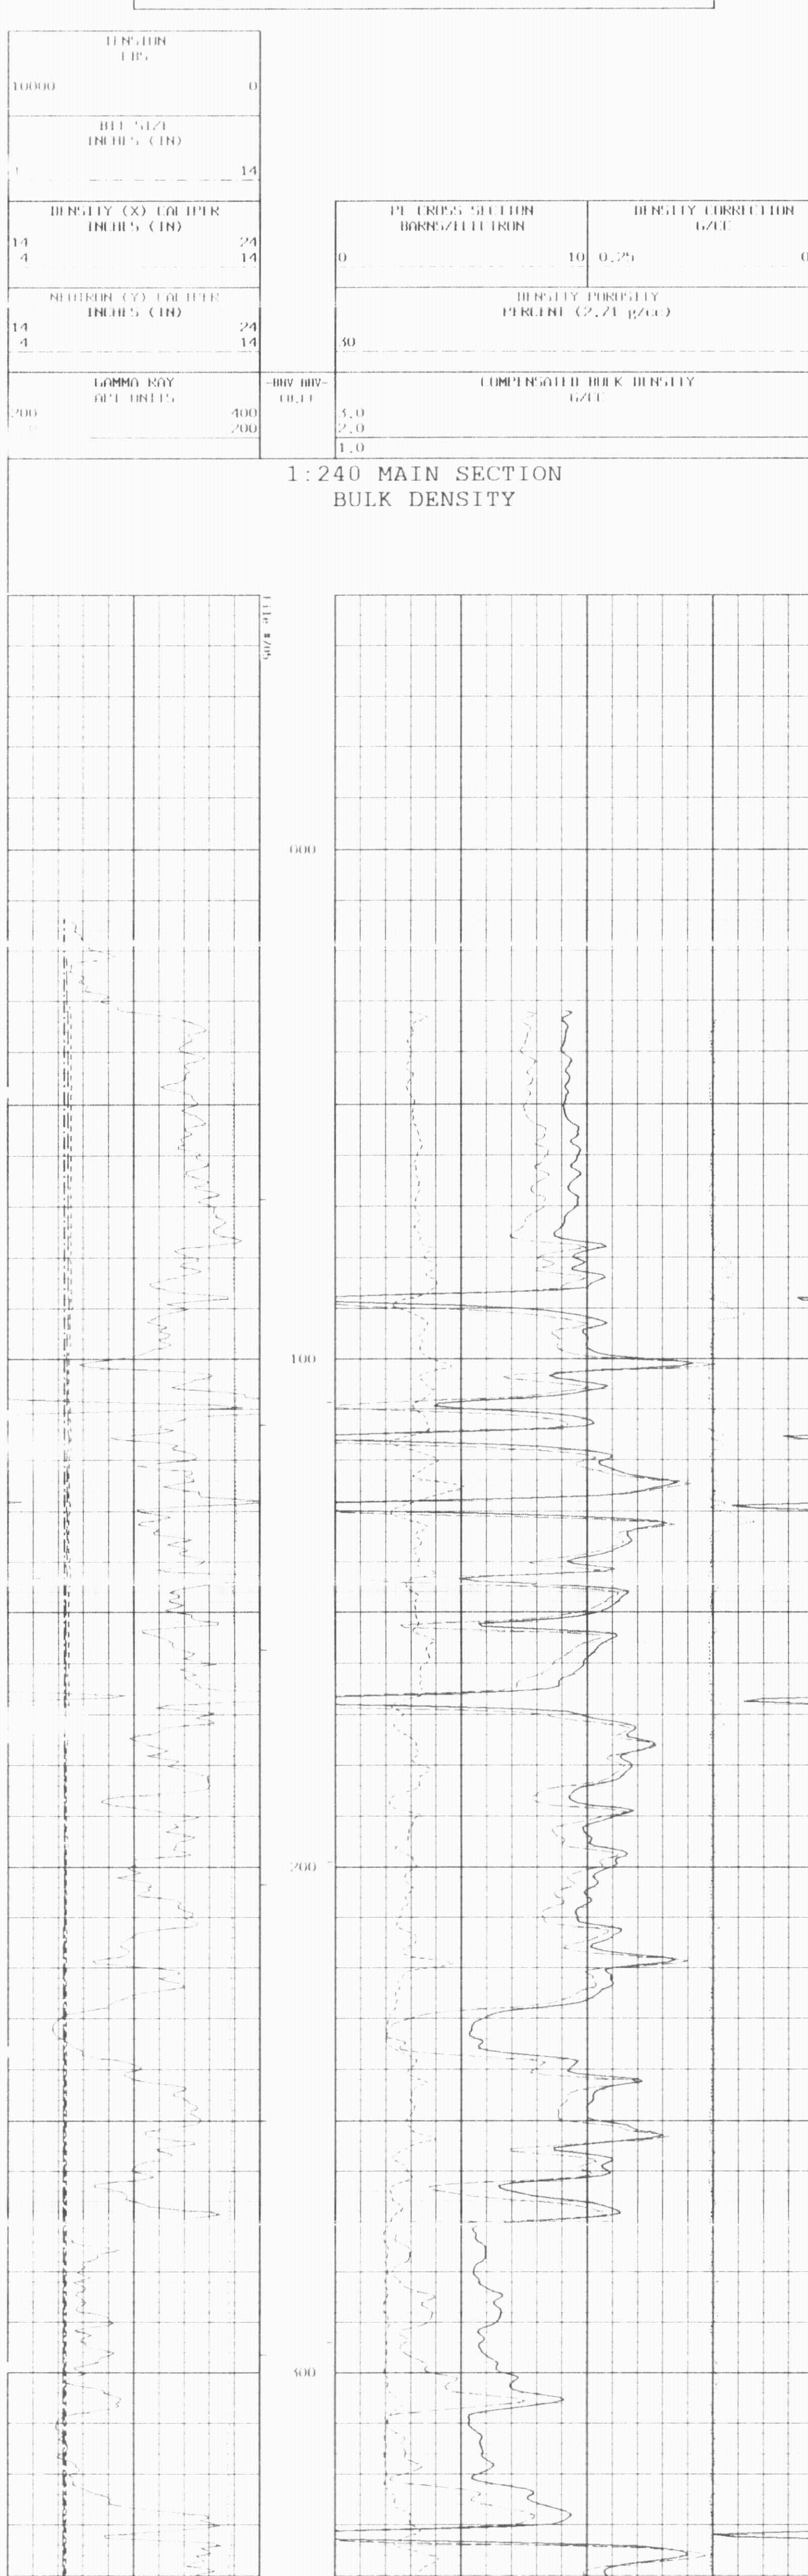

1:240 MAIN SECTION
BULK DENSITY
