317-22729

RECEIVED

MAY 19 2011

Mo Oil & Gas Council

MIDWEST SURVEYS

LOGGING - PERFORATING - CONSULTING SERVICES
P.O. Box 68, Osawatomie, KS 66064
913 / 755 - 2128

GAMMA RAY / CEMENT BOND / CCL

API # 24-217-22.729

File No.

Company	Mega West Energy
Well	Johnson No. GC-2P1
Field	Grassy Creek Project
County	Vernon State Missouri

4/9/12

Location: 622' FSL & 1456' FWL, SW/4

Sec. 16 Twp. 35n Rge. 33w

Other Services

Permanent Datum	GL	Elevation	829'
Log Measured From	GL		
Drilling Measured From	GL		

Elevation: K.B. NA, D.F. NA, G.L. 829'

Date	04-25-2011				
Run Number	One				
Depth Driller	283.0				
Depth Logger	277.6				
Bottom Logged Interval	274.6				
Top Log Interval	20.0				
Fluid Level	Full				
Type Fluid	Water				
Density / Viscosity	NA				
Salinity - PPM Cl	NA				
Max Recorded Temp	NA				
Estimated Cement Top	NA				
Equipment No.	Location	107	Osawatomie		
Recorded By	Steve Windrsch				
Witnessed By	Jim Long				

RUN	BORE-HOLE RECORD			CASING RECORD			
No.	BIT	FROM	TO	SIZE	WGT	FROM	TO
One	10.00"	0.0	40.0	8.625"	20 #	0.0	40.0
Two	8.00"	40.0	283.0	5.50"	17 #	0.0	280.0

<<< Fold Here >>>

All interpretations are opinions. Based on inferences from electrical or other measurements and we cannot and do not guarantee the accuracy or correctness of any interpretation, and we shall not be liable or responsible for any loss, costs, damages or expenses incurred or sustained by anyone resulting from any interpretation made by any of our officers, agents or employees. These interpretations are also subject to our general terms and conditions set out in our current Price Schedule.

Comments
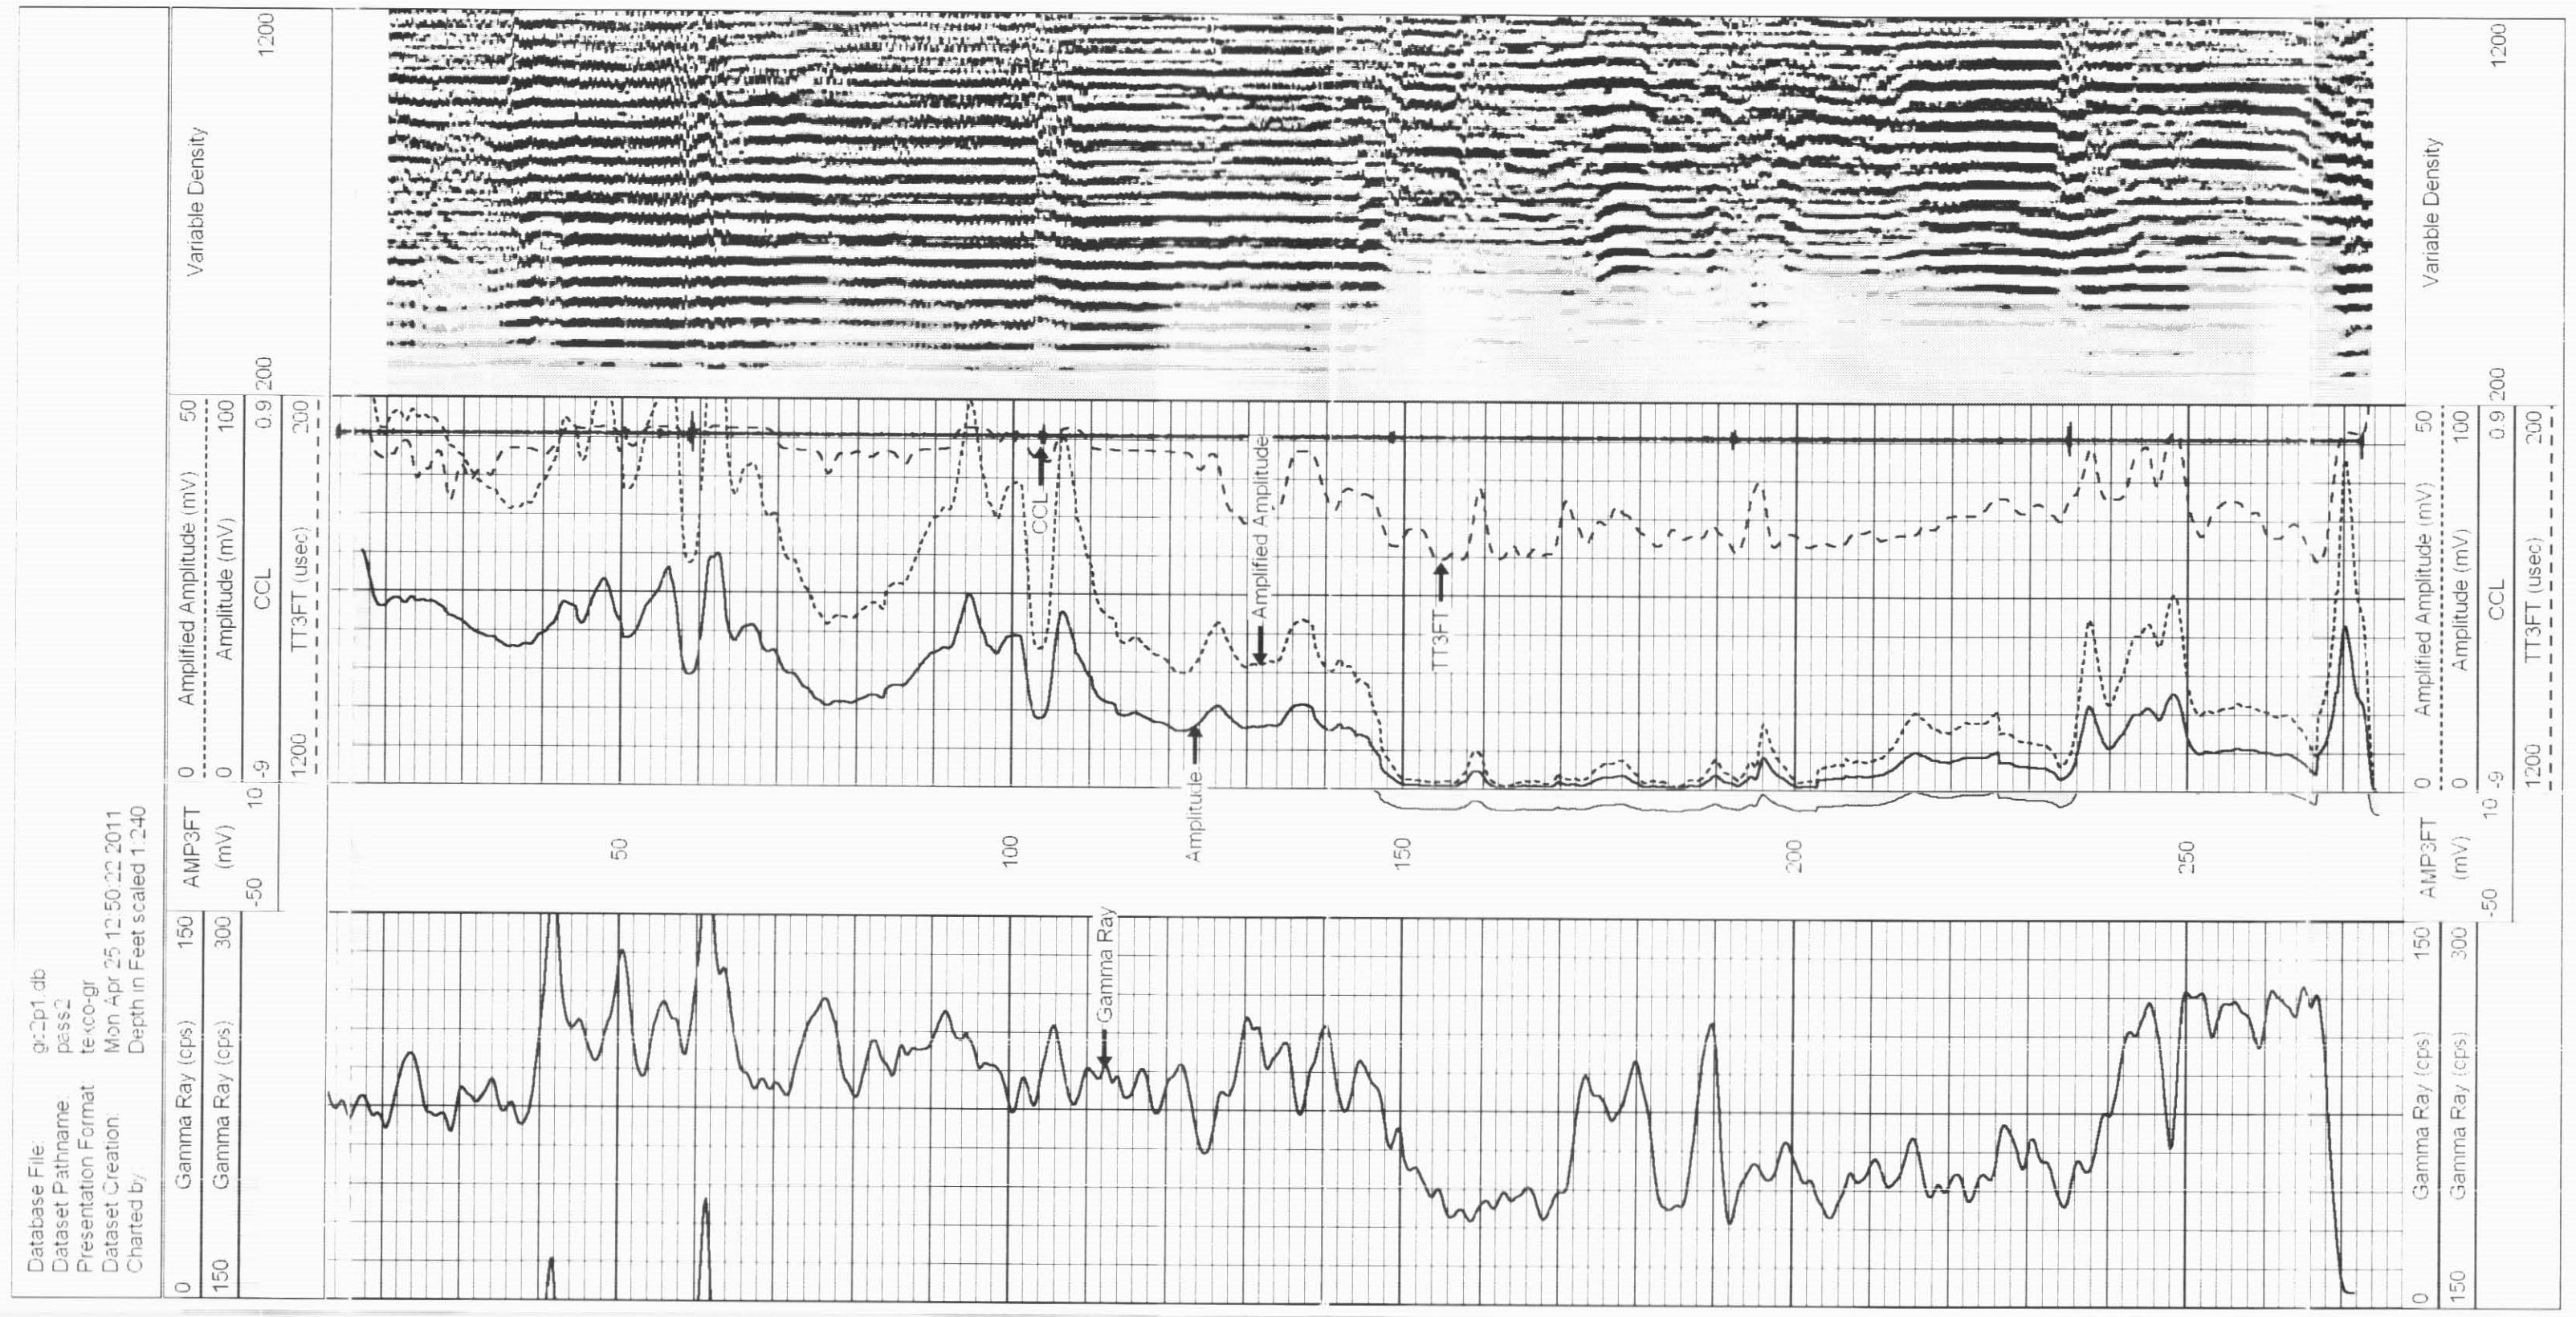
Drilling Contractor : Action Drilling
