county DAVIESS

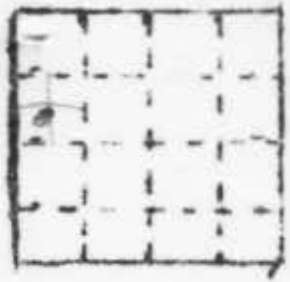

sec 5 twp 59 rge 27

owner Shaffer, J.K.D.

elev 759 ~~MGS#~~ Drillers Log ~~rge~~ 8

farm Tingler, A.J. No. 1 TD 2332 fm TD * shows So (+)

status d & a. date completed 9 AUG 1919

remarks: */ Canadian & older

(+) Show repted by driller

p151 Vol. XXV

CCCD 3

00001

DAVIESS COUNTY
No. 3918

Owner: J.K.D. Shaffer Co.
Location: Sec. 5, T. 59 R. 27, Well No. 1 A. J. Tingler Farm.
Elevation: 734
Depth: 2332 feet.
Driller: Henry Rosenthal.
Hole spudded: March 23, 1919 : Completed Aug. 9, 1919.
Record submitted by : W. R. Handy, Gallatin, Mo. Sept. 8. 1932.
Remarks: Strip log made.

Soil, black	4	4
Clay, yellow	38	34
Sand, brown	40	2
Sand, brown	46	6
H.F.W. at 42'		
Set 15 1/2 " casing at 43'7"		
Blue slate	80	34
Blue slate	100	20
Lime, white	104	4
Slate, white	124	20
Lime, white	130	6
Slate, blue	140	10
Slate, blue	160	20
Lime, white	200	40
Coal	202	2
Slate, black	206	4
Slate, white=	226	20
Lime, white	266	40
Set 12 1/2 " casing at 238		
Slate, blue	276	10
Lime, white	306	30
Slate, blue	310	4
Slate, blue	316	6
Lime, white	331	15
Water, 3 bailers per hour at 320		
Slate, white	339	8
Coal, black	342	3
Slate, white	354	12
Lime, white	358	4
Slate, black	364	6
Slate, white	374	10
Lime, white	379	5
Slate, black	394	15
Lime, white	408	14
Slate, brown	428	20
Slate, brown	438	10
Slate, black	468	30
Lime, white	483	15
Slate, black	508	25
Lime, white	528	20
Slate, blue	558	30
Lime, white	568	10
Lime, white	588	20
2 bailers per hour at 570 carrying 8 bailers.		
3 bailers per hour at 528 feet.		
Slate, brown,	623	35
Slate, white	648	25
Lime, white	650	2
Lime, white	653	3
Slate, white	663	10
Lime, white	670	7
H.F.W. at 670 set 10" at 670		
Sand, white	686	16
Sand, white	701	15
Lime, white	756	55
H.F.W. at 750		
Lime, white	800	44
Lime, white	830-	30
Miss. lime	860	30
Miss Lime	900	40
Miss. lime	950	50
Miss. lime	990	40
Miss. lime	1020	30
Slate, white	1025	5
Set 8 " casing at 1015'11"		
Slate, white	1065	40
Sand, white	1070	5
Slate, blue	1085	15
Lime, white	1105	20
Slate, white	1130	25
Slate, white	1200	70
U.R. 8" casing to 1162' 4"		
Slate, white	1230	60
Sand, white	1270	10
15 bailers per hr. at 1270. Hole caving		
No log	1280	10

1020
734
286

PL

Slate	1290	10
Lime, brown	1300	10
Water at 1295		
Lime, brown	1310	10
Lime, brown	1330	20
Lime, brown	1340	10
Broekn lime	1355	15
Miss. Lime	1360	5
Lime	1380	20
Slate, white	1385	5
Hard, lime	1395	10
Lime	1400	5
broken lime	1405	5
sharp sandy lime	1430	25
sharp sandy lime	1460	30
Sandy lime	1470	10
Lime	1490	20
Lime	1500	10
Lime	1540	40
Lime	1550	10
Brown sand	1570	20
Brown, sand	1575	5
White water sand	1605	30
Water sand	1650	45
Water sand	1675	25
Lime	1740	65
sandy lime	1765	25
Sandy lime	1785	20
10 days of drilling July 8 to 17, 1919.		
No record given 1785-2070		
sandy lime	2100	30
Sandy lime	2190	90
sandy lime	2200	10
sandy lime	2230	30
sandy lime	2332	102

T.D. 2332

Shut down - pipe pulled- hole abandoned 8/16/19
